

Job Number: 20/0071
Record No.: CC-0002**CHANGE IN CONTRACT**

Harris County Flood Control District

Contractor:	HURTADO CONSTRUCTION CO	Date:	7/21/2021			
Address:	2115 Center Street Richmond, TX	PO Number:	P0000001189			
		PS Fund:				
		PS Activity:				
Project Name:	Excavation of Little York Basin and Hopper Basin and Channel Conveyance Improvements in P118-14-00					
Project ID:	P518-10-00-E002					
<p>Contractor: In connection with your contract dated 5/19/2020, for construction of the above mentioned job, the work or material outlined below was not comprehended in the original contract, or the following deduction is desired. When this order has been properly filled in, and approved, please proceed to do this work in accordance with the alterations set out below:</p>						
Description of Change Desired						
<p>This contract change includes extension of quantities for tires discovered onsite in excess of planned quantities. Additionally, a homeless encampment was found onsite, and a new scope of work is added for the removal and disposal of trash and debris associated with the cleanup of the encampment. The proposed unit prices were reviewed, validated, and found to be acceptable. During construction, it was found that the 42" RCPs to be installed as per the plans were incorrect. 72" RCPs were existing onsite and are added to the contract in place of the planned 42" pipe. To mitigate an existing water ponding issue, 24" RCP is proposed under the access site grading. Proposed 3'x2' Reinforced Concrete Box culverts were shown on the plans to be installed, however, 24" RCPs with SETs were existing onsite. Those culverts are proposed to be extended with 24" RCP. The plans specify 8" Thick Hot Mix Asphalt Base Course. During construction, it was identified that there was no 8" Hot Mix Asphalt Surface called for in the project plans. HCFCD maintenance and infrastructure requests an all-weather access road from US-59 frontage road to weir/floatable collecting structure.</p> <p>The 81-day time extension is a sum of six days for trash & tire disposal, 44 days for inclement weather from April 1, 2021, through July 31 2021, 12 days for 72" pipe installation, 6 days to correct ponding, two days for additional surface course and 11 days to construct the added all weather access road,</p> <p>These changes have been discussed and agreed to by the contractor, Construction Project team, Engineer of Record and HCFCD Design Program Manager. The modifications of work and extensions of work result in a net increase of \$264,036.42 to the contract purchase order amount and 81 days added to the contract duration.</p>						
Estimate of Cost						
Change Type	Pay Item ID	Pay Item Name	Unit	Quantity	Unit Price	Amount
Decrease	02612-10	3 x 2 REINFORCED CONCRETE BOX	LF	-272.00	188.00	-51,136.00
	02611-05	42-INCH REINFORCED CONCRETE PIPE	LF	-248.00	138.00	-34,224.00
					Subtotal	-85,360.00
Increase	02611-02	24-INCH REINFORCED CONCRETE PIPE	LF	256.00	76.00	19,456.00
	02365-01	STABILIZED CONSTRUCTION ACCESS	SY	3,722.00	28.00	104,216.00
	02712-01	CEMENT STABILIZED BASE COURSE	SY	3,285.00	18.88	62,020.80
	02611-02	24-INCH REINFORCED CONCRETE PIPE	LF	69.00	76.00	5,244.00
					Subtotal	190,936.80
Addition	02315-06	BACKSLOPE DRAINAGE SYSTEM SWALES	LF	175.00	6.06	1,060.50
	02120-09	REMOVE & DISPOSE OF TIRES <= 16	EA	641.00	7.88	5,051.08

County Auditor's Form 1258
Harris County TX (REV. 5/17/2017)

02120-10	REMOVE & DISPOSE OF TIRES >16	EA	38.00	9.88	375.44
02120-30	REMOVE & DISPOSE OF TIRES, 13 TO 16 RIM DIAMETER	EA	39.00	11.00	429.00
02120-02	DEBRIS AND TRASH REMOVAL AND DISPOSAL IN A LANDFILL	CY	880.00	23.88	21,014.40
02632-74	REMOVE AND RESET SAFETY END TREATMENT	EA	8.00	200.00	1,600.00
02611-10	72-INCH REINFORCED CONCRETE PIPE	LF	240.00	473.58	113,659.20
02741-02	ASPHALTIC CONCRETE PAVEMENT, 2 THICKNESS	SY	600.00	25.45	15,270.00
		Subtotal			158,459.62
	Changes in Calendar days: 81				

TOTAL ADDED TO CONTRACT:	349,396.42
TOTAL DEDUCTED FROM CONTRACT:	-85,360.00
NET CHANGE:	264,036.42

If applicable, the Auditor's certification is made when the purchase order is amended in the system.

DocuSigned by:
Approved: Bruce Dinkheller
1A350B664318439...

Print Name: Bruce Dinkheller
Project Manager

Basis and Work Agreeable to Us.

DocuSigned by:
Approved: Alan Black
2E985FDADEC4476...


Print Name: Alan Black
HCFC, Executive Director

Contractor: HURTADO CONSTRUCTION CO

Signed: Miguel Hurtado
7FE4BA06C189443...
For the Contractor

Print Name: Miguel Hurtado

Authorized in Minutes Of: _____

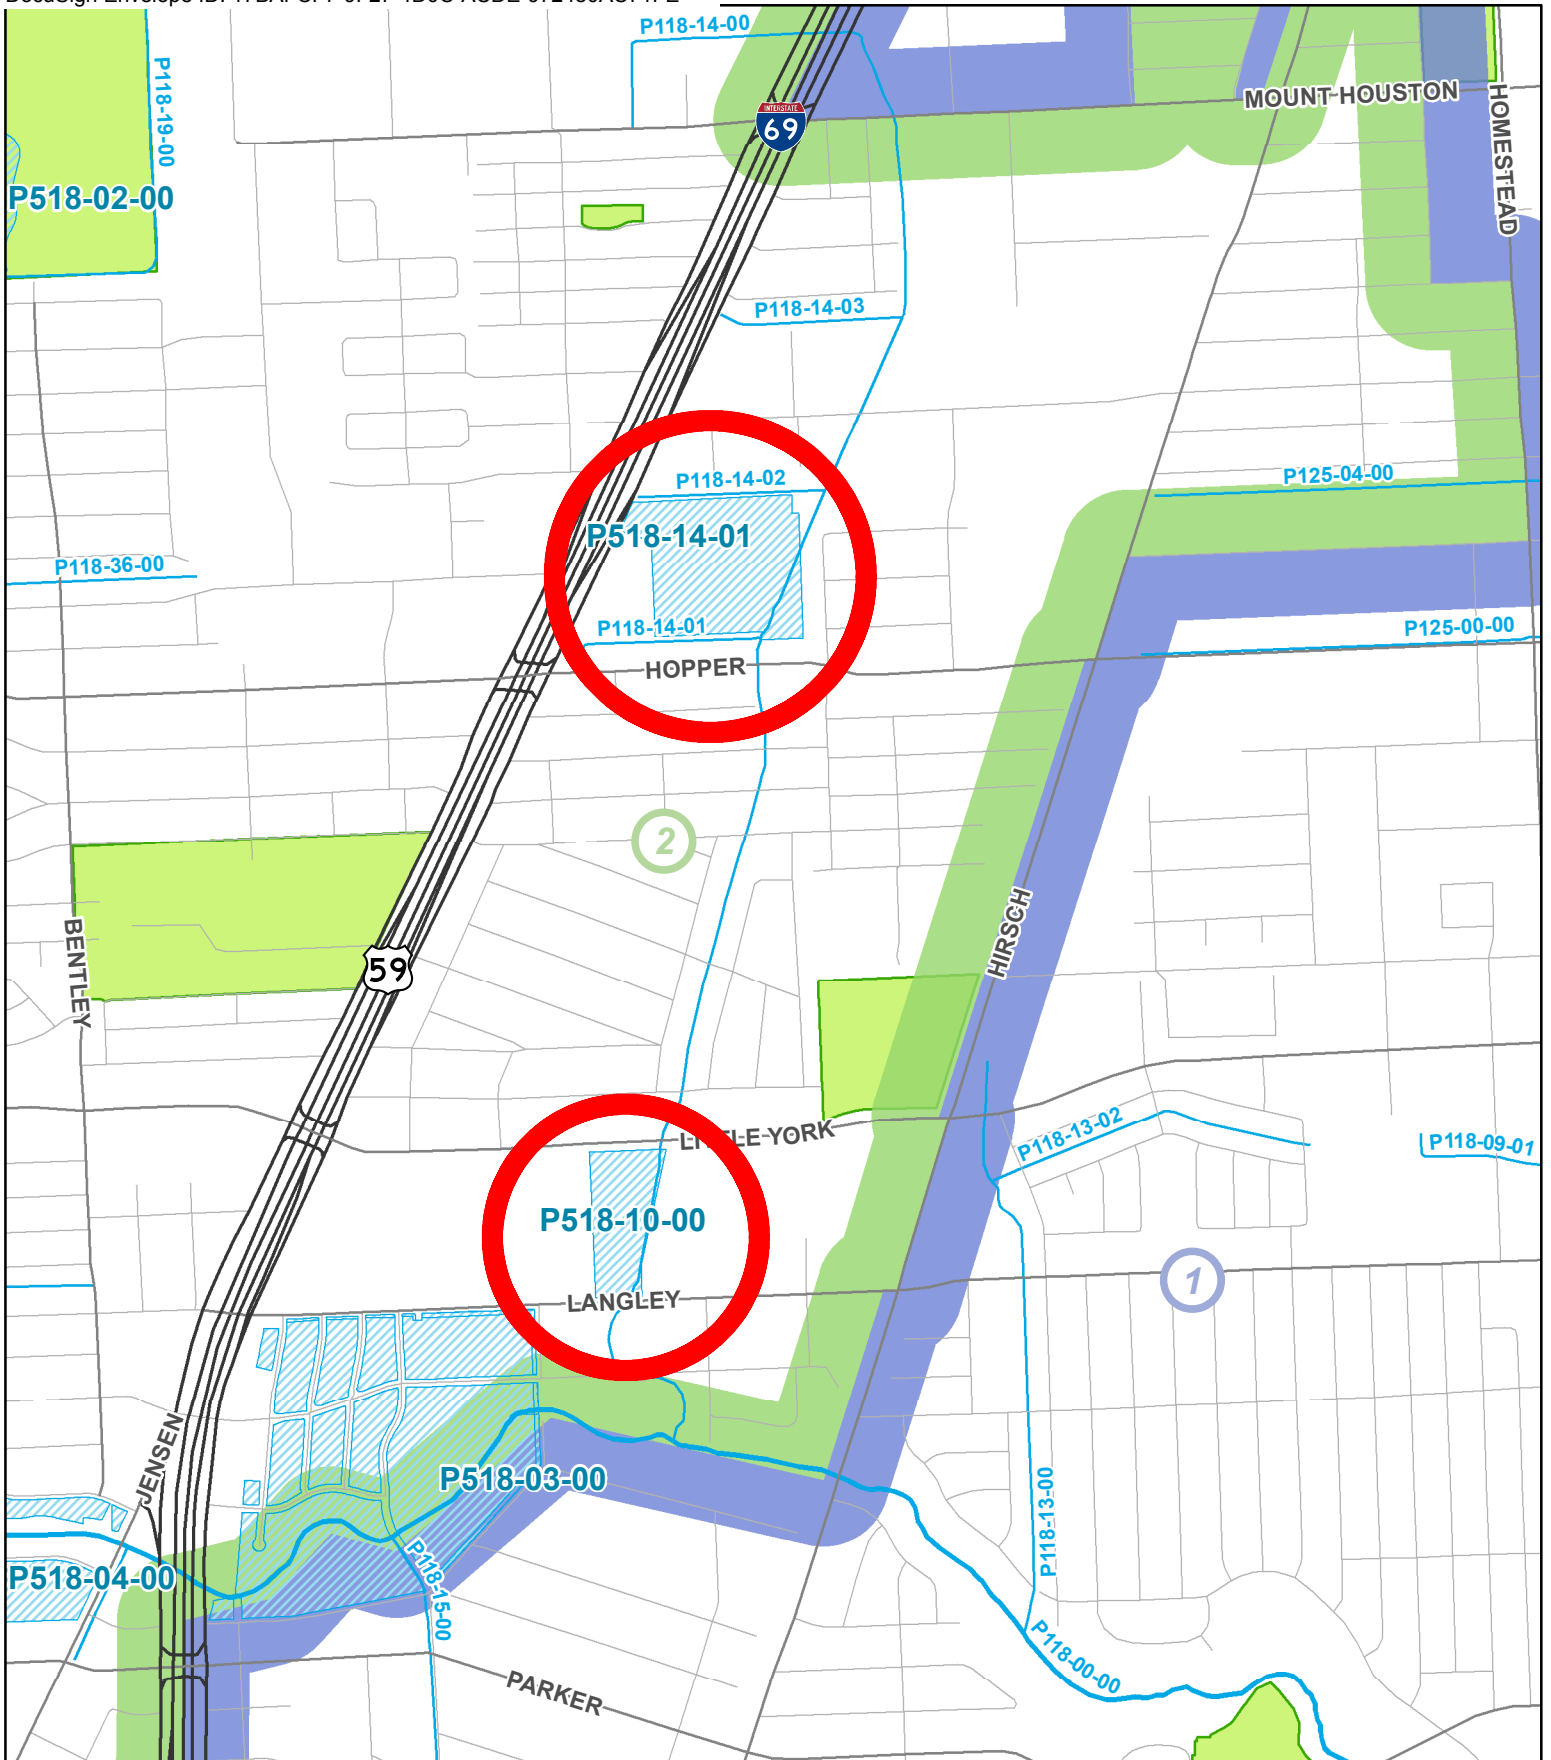

Project ID: P518-10-00-E002
Watershed: Halls Bayou
Precinct: 2

Pct No

-  1
-  2
-  3
-  4

