

Job Number: 21/0078
 Record No.: CC-0003

CHANGE IN CONTRACT

Harris County Flood Control District

Contractor:	Lecon, Inc.	Date:	8/5/2022
Address:	4302 CREEKMONT DR	PO Number:	P0000002183
	HOUSTON, TX	PS Fund:	
	77091-5330	PS Activity:	
Project Name:	Drainage Improvements Phase I Excavation of P518-11-00 Detention Basin		
Project ID:	P518-11-00-E001		



Contractor: In connection with your contract dated 6/8/2021, for construction of the above mentioned job, the work or material outlined below was not comprehended in the original contract, or the following deduction is desired. When this order has been properly filled in, and approved, please proceed to do this work in accordance with the alterations set out below:

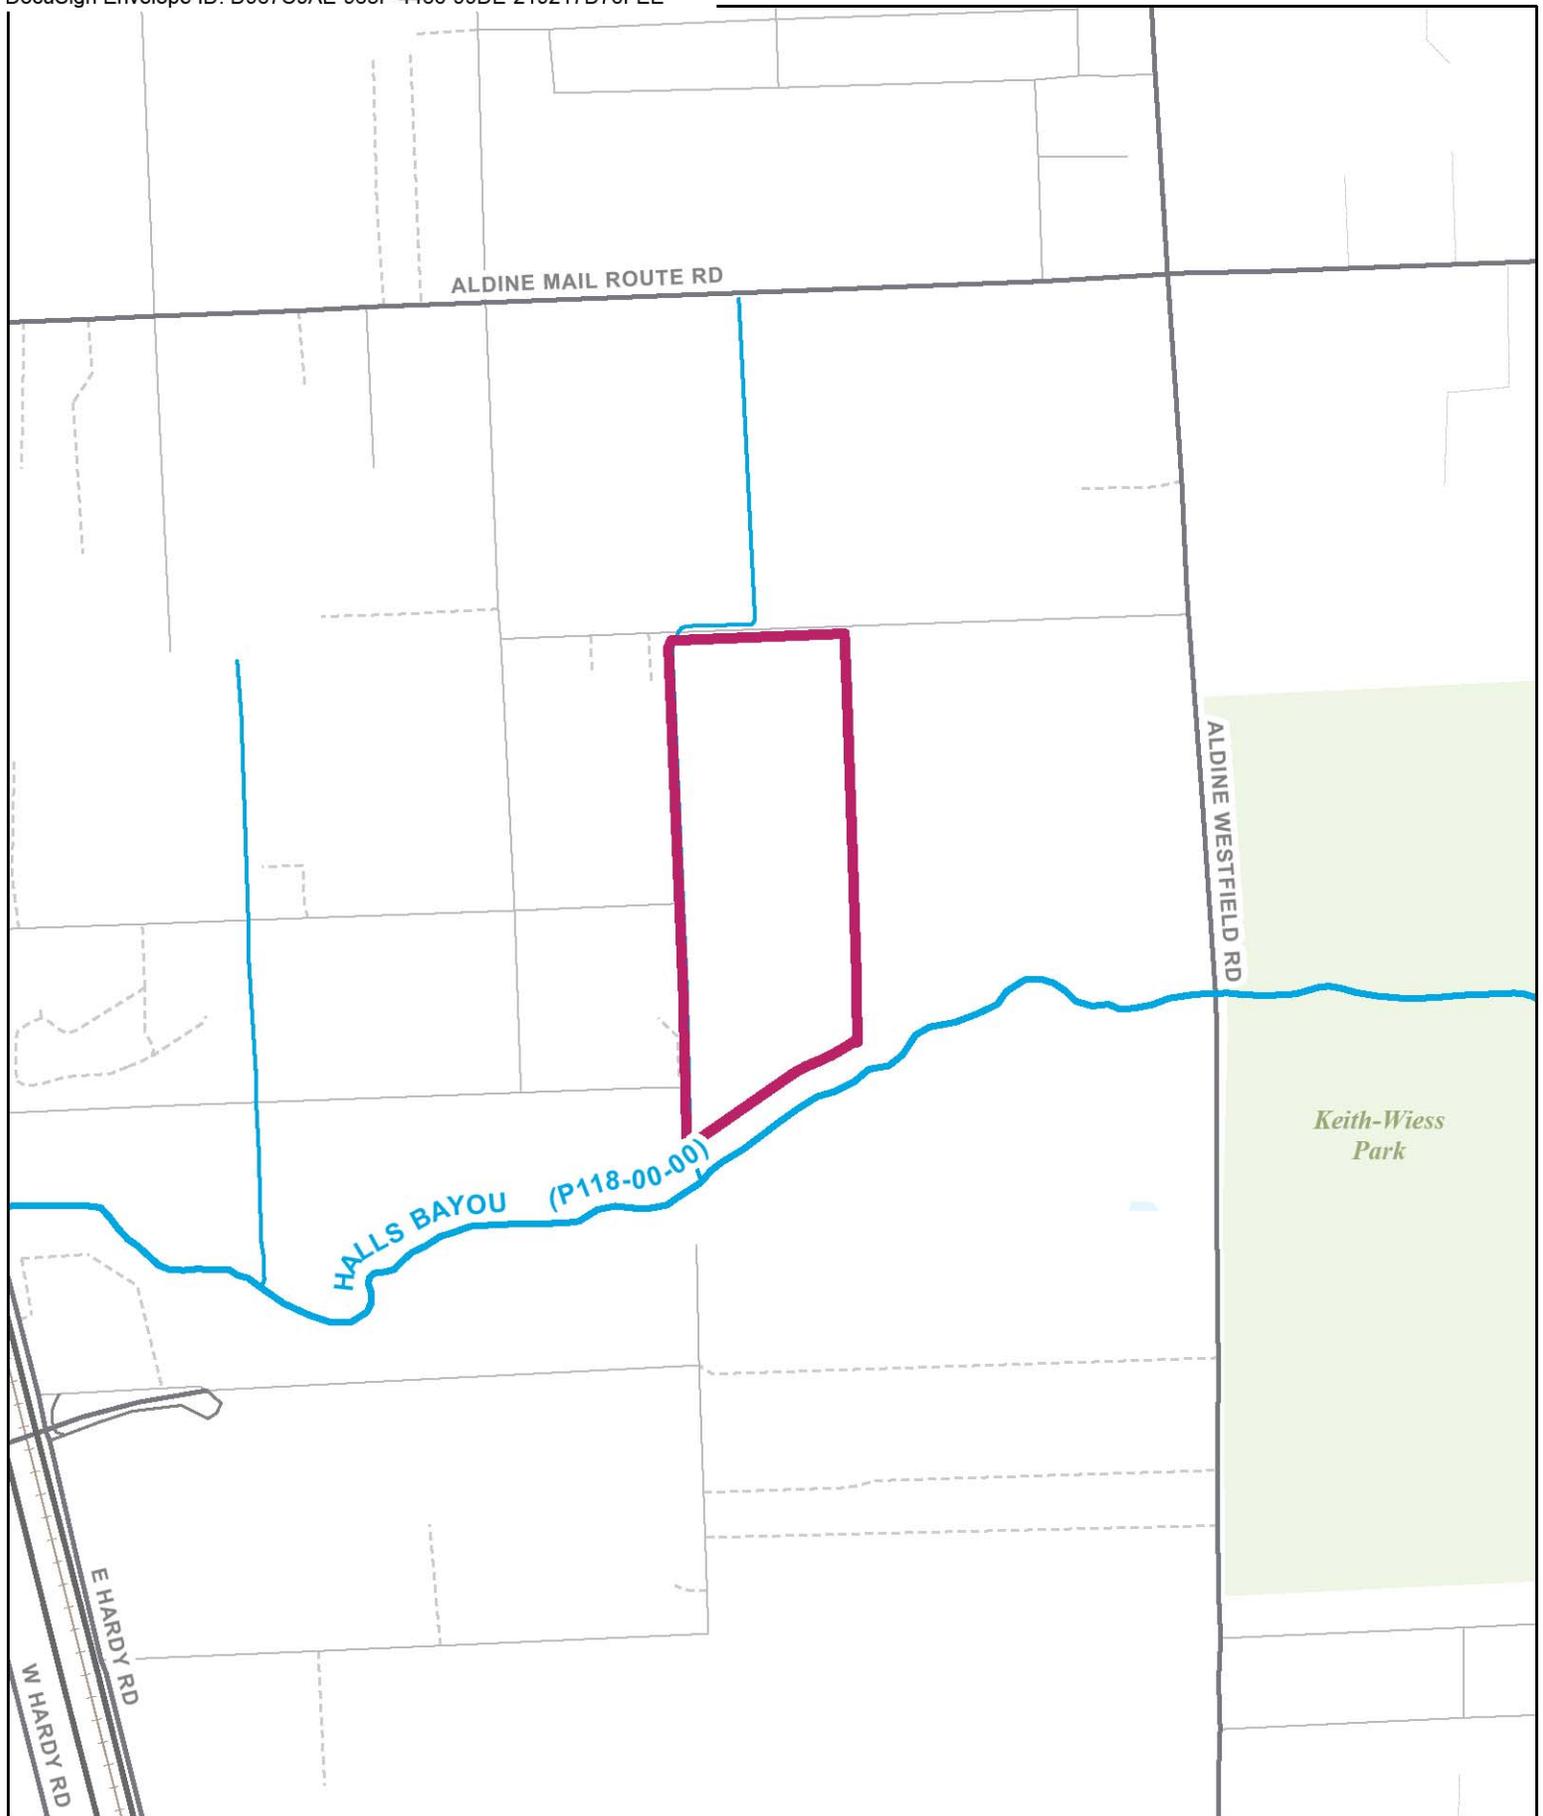
Description of Change Desired

The purpose of this contract change is to extend the contract duration by a total of 31 days. Due to administrative delays the original targeted Commissioners' Court date of 5 April 2022 was missed and the contract change delayed until 26 April 2022. As a result, the project critical path was impacted and an additional 20 days is requested due to this delay. 11 days are due to inclement weather impacting critical path from 16 March to 15 May 2022.

Estimate of Cost

Change Type	Pay Item ID	Pay Item Name	Unit	Quantity	Unit Price	Amount
Decrease						
	Subtotal					0.00
Increase						
	Subtotal					0.00
Addition						
	Subtotal					0.00
		Changes in Calendar days: 31				

	TOTAL ADDED TO CONTRACT:	0.00
	TOTAL DEDUCTED FROM CONTRACT:	0.00
	NET CHANGE:	0.00
If applicable, the Auditor's certification is made when the purchase order is amended in the system.	Approved: 	
	Print Name: Lucia L. Lee Project Manager	
Basis and Work Agreeable to Us.	Approved: 	
	Print Name: Tina Petersen HCFC, Executive Director	
Contractor: Lecon, Inc.		
Signed: 		
Print Name: Shawn Schmitt/Lecon		
	Authorized in Minutes Of: _____	



Project ID: P518-11-00-E001
Watershed: Halls Bayou
Precinct: 2

- Project Boundary
- Harris County Precincts**
- Judge Lina Hidalgo
- 1 - Rodney Ellis
- 2 - Adrian Garcia
- 3 - Tom S. Ramsey, P.E.
- 4 - R. Jack Cagle

