

Job Number: 20/0270
Record No.: CC-0002

CHANGE IN CONTRACT

Harris County Flood Control District

Contractor:	R Miranda Trucking and Construction LLC	Date:	10/21/2021
Address:	6326 PERCH CREEK DR HOUSTON, TX 77049-3441	PO Number:	P0000001530
		PS Fund:	
		PS Activity:	
Project Name:	M124-00-00 Channel Excavation from SH249 to FM2920 and Stormwater Detention Basin Phase I		
Project ID:	M124-00-00-E001		

Contractor: In connection with your contract dated 11/10/2020, for construction of the above mentioned job, the work or material outlined below was not comprehended in the original contract, or the following deduction is desired. When this order has been properly filled in, and approved, please proceed to do this work in accordance with the alterations set out below:

Description of Change Desired

The purpose of this change in contract is to address changes encountered in the field. The installation of a new live gas line under a privately owned road by jack and bore/directional drilling required an extension of the temporary bypass be added to work scope. The drilling process also required excavation of two 20ft by 25ft by 5ft deep pits to make the connection of the new gas pipeline to the existing gas pipeline. As a result, 4 ft of additional pipe was needed to complete the pipeline connection, and the temporary access road, composed of 3x5 granular fill and crushed limestone, had to be adjusted and extended so citizens traveling along the private road to their homes could travel around the two pipeline tie-in pits and related equipment. This temporary access road work adds 6 days to the project duration. An extension of HDPE pipe is needed for a field fit adjustment to a planned interceptor structure which conflicted with an existing storm water drainage pipe in the initial planned location. The planned quantity of testing of unknown pipelines was not needed to the full planned quantity and has been reduced. Lastly, the contractor has experienced 16 days of inclement weather that has impacted the contractor's critical path. The adjustment to 3x5 granular fill, the crushed limestone, the HDPE pipe and the gas pipeline and reduced scopes of work have been agreed to by the Construction team, the Design Project manager, the Engineer of Record, and the Contractor. The modified work scope results in a net increase of \$0 to the contract Purchase Order amount and 22 days added to the contract duration.

Estimate of Cost


Change Type	Pay Item ID	Pay Item Name	Unit	Quantity	Unit Price	Amount
Decrease	02224-01	TESTING AND DETERMINATION OF THE STATUS OF UNKNOWN PIPELINES	EA	-11.61	2,500.00	-29,014.50
	Subtotal					-29,014.50
Increase	02445-01	JACK, BORE OR TUNNEL PIPE	LF	4.00	124.00	496.00
	02711-01	CRUSHED LIMESTONE FLEXIBLE BASE COURSE, 6 THICKNESS	SY	827.00	15.50	12,818.50
	02378-10	GRANULAR FILL, 3-5 INCHES	SY	520.00	22.50	11,700.00
	02505-02	24-INCH HIGH DENSITY POLYETHYLENE (HDPE) SOLID AND PROFILE WALL PIPE	LF	50.00	80.00	4,000.00
Subtotal					29,014.50	
Addition						
	Subtotal					0.00

County Auditor's Form 1258
Harris County TX (REV. 5/17/2017)

	Changes in Calendar days: 22	
--	------------------------------	--

<p>If applicable, the Auditor's certification is made when the purchase order is amended in the system.</p>	<table style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 80%;">TOTAL ADDED TO CONTRACT:</td> <td style="text-align: right;">29,014.50</td> </tr> <tr> <td>TOTAL DEDUCTED FROM CONTRACT:</td> <td style="text-align: right;">-29,014.50</td> </tr> <tr> <td>NET CHANGE:</td> <td style="text-align: right;">0.00</td> </tr> </table> <p>Approved: DocuSigned by: <i>Mondel Garcia</i> 982F3EFC1BBE415...</p> <p>Print Name: <u>Mondel Garcia</u> <u>Project Manager</u></p>	TOTAL ADDED TO CONTRACT:	29,014.50	TOTAL DEDUCTED FROM CONTRACT:	-29,014.50	NET CHANGE:	0.00
TOTAL ADDED TO CONTRACT:	29,014.50						
TOTAL DEDUCTED FROM CONTRACT:	-29,014.50						
NET CHANGE:	0.00						
<p style="text-align: center;">Basis and Work Agreeable to Us.</p> <p>Contractor: R Miranda Trucking and Construction LLC</p> <p>Signed: DocuSigned by: <i>Roberto Miranda</i> 1FF1B383C1A2047E...</p> <p style="text-align: center;">For the Contractor</p> <p>Print Name: <u>Roberto Miranda</u></p>	<p>Approved: DocuSigned by: <i>Alan Black</i> 2E985FD0ADEC4476...</p> <p>Print Name: <u>Alan Black</u> <u>HCPCD, Executive Director</u></p> <p>Authorized in Minutes Of: _____</p>						



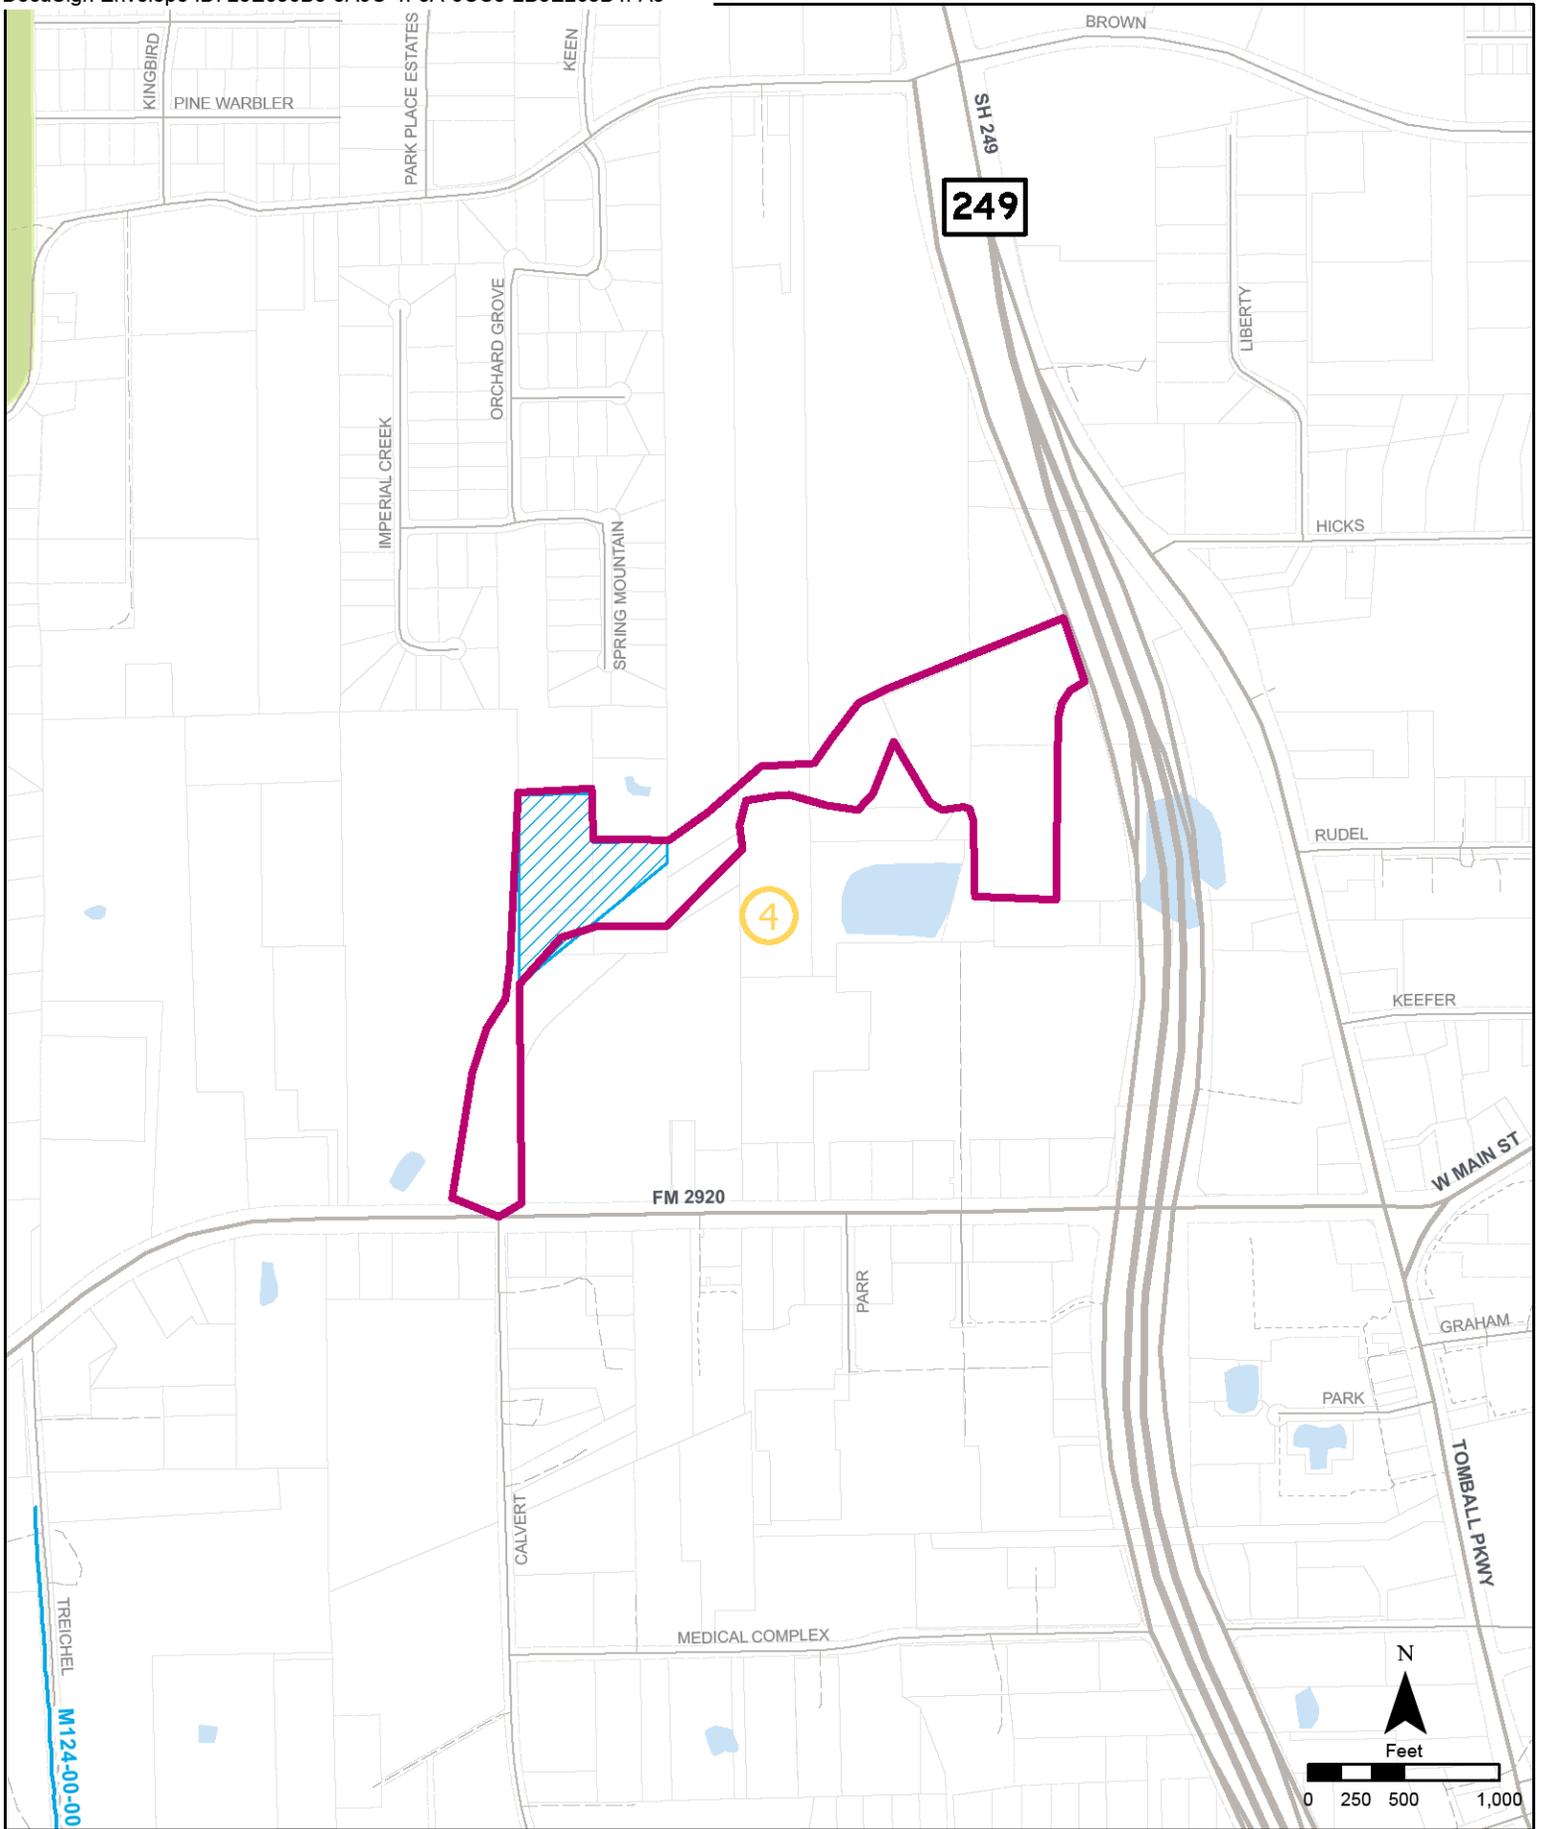

Project ID: M124-00-00-E001

Watershed: Willow Creek
Precinct: 4

