

CHANGE IN CONTRACT

Harris County Flood Control District

Contractor: James Construction Group, LLC	Date: 03/30/2021
Address: 222 Pennbriht Drive Houston, TX 77090	PO Number: P307444
	OrgKey: 33109021
	ObjCode: 637800
Project: Brays Bayou Federal Flood Control Project Stella Link Bridge Extension and Ardmore Bridge Replacement On Brays Bayou Discrete Segme	
I.D. No.: D100-00-00-B027 UPIN180900D1B027	

Contractor: In connection with your contract dated 8/14/2018, for construction of the above mentioned job, the work or material outlined below was not comprehended in the original contract, or the following deduction is desired. When this order has been properly filled in, and approved, please proceed to do this work in accordance with the alterations set out below:

Description of Change Desired

The purpose of this Contract revision is to adjust bid item quantities for completed scopes of work. The adjustment accounts for changes in scope due to unforeseen field conditions (grade difference between trail and ramp, elevation of channel modification connections, condition of existing structures, location of existing utilities), and HCFCD scope revision which resulted in additional work and added pay items. The added scope included COH requested additional traffic signs and pipe guard to enhance public commuter and pedestrian safety for the Ardmore Bridge signals and Stella Link WL crossing.

This revision modifies general conditions SC-5.8 and SC-4.17.3.6 by extending the contract warranty period by an additional (1) one calendar year due to the Ardmore bridge deck clear cover remediation. This change in contract results in a net increase of \$41,923.40 to the Contract PO amount and no additional calendar days.

Refer to Variances 41, 42, 43, 44, 45 for information.

Estimate of Cost

Pay Item	Description	Unit	Quantity	Unit Price	Amount
Extend:					
0428-01	Conc Surf Treat	SF	2576.9200	\$0.51	1,314.23
0450-52	Pedestrian Rail	LF	20.0000	\$87.98	1,759.60
	(421 TXDOT) (440 TXDOT) (442 TXDOT) (445 TXDOT) (446 TXDOT) (540 TXDOT)				
2120-26	Remove & Dispose of Driveways and Sidewalks (01565)	SY	4.6700	\$14.00	65.38
2200-05	Site Preparation & Restoration (01520) (01565) (01580) (02120) (02233) (02241)	EA	0.4586	\$15,000.00	6,878.49
2376-03	Concrete Channel Lining, 6" (02316) (03310)	SY	115.6500	\$67.94	7,857.26
2379-05	Geotextile, Non-woven	SY	97.0400	\$4.90	475.50
2379-20	Geogrid	SY	97.0400	\$5.92	574.48
2630-60	Adjust Manholes/Inlets to Grade (02120) (02316) (02321) (03310)	EA	3.0000	\$1,848.25	5,544.75
2714-10	Crushed Limestone Flexible Base Course, 4" (02316)	SY	97.0400	\$15.32	1,486.65
2775-01	Concrete Sidewalk (02316) (02752) (03310)	SF	81.8300	\$9.53	779.84
2893-02	Traffic Signs & Signals (02465)(02582)(05501)(16710)(16711)(16715)(16719)(16727) (16730)(16731)(16732)(16	EA	0.0305	\$176,350.00	5,385.91
				subtotal	32,122.08
Add:					
1555-02	Flagperson	DA	6.0000	\$404.70	2,428.20
2525-02	Test Hole	EA	3.0000	\$1,190.32	3,570.96

CHANGE IN CONTRACT

Harris County Flood Control District

Estimate of Cost

Pay Item	Description	Unit	Quantity	Unit Price	Amount
2642-60	Bar Guard, 24" Pipe (Plans)	EA	1.0000	\$3,802.16	3,802.16
subtotal					9,801.32
Changes In Calendar Days:		0			

TOTAL ADDED TO CONTRACT:	\$41,923.40
TOTAL DEDUCTED FROM CONTRACT:	\$0.00
NET CHANGE:	\$41,923.40

If applicable, the Auditor's certification is made when the purchase order is amended in the system.

Approved:

DocuSigned by:
Nathan Hayden 4/8/2021

8DA153B6E4794CD...
Nathan Hayden, PE, Director, Construction Division

Basis and Work Agreeable to Us.


Contractor: James Construction Group, LLC
DocuSigned by:
Rik van den Berg 4/9/2021
C95C5A2879654ED...

For the Contractor

Print Name: Rik van den Berg

DocuSigned by:
Russell A Poppe 4/12/2021
4BD1C2EDFD264B7...
Russell Poppe, Executive Director

Authorized in Minutes of _____

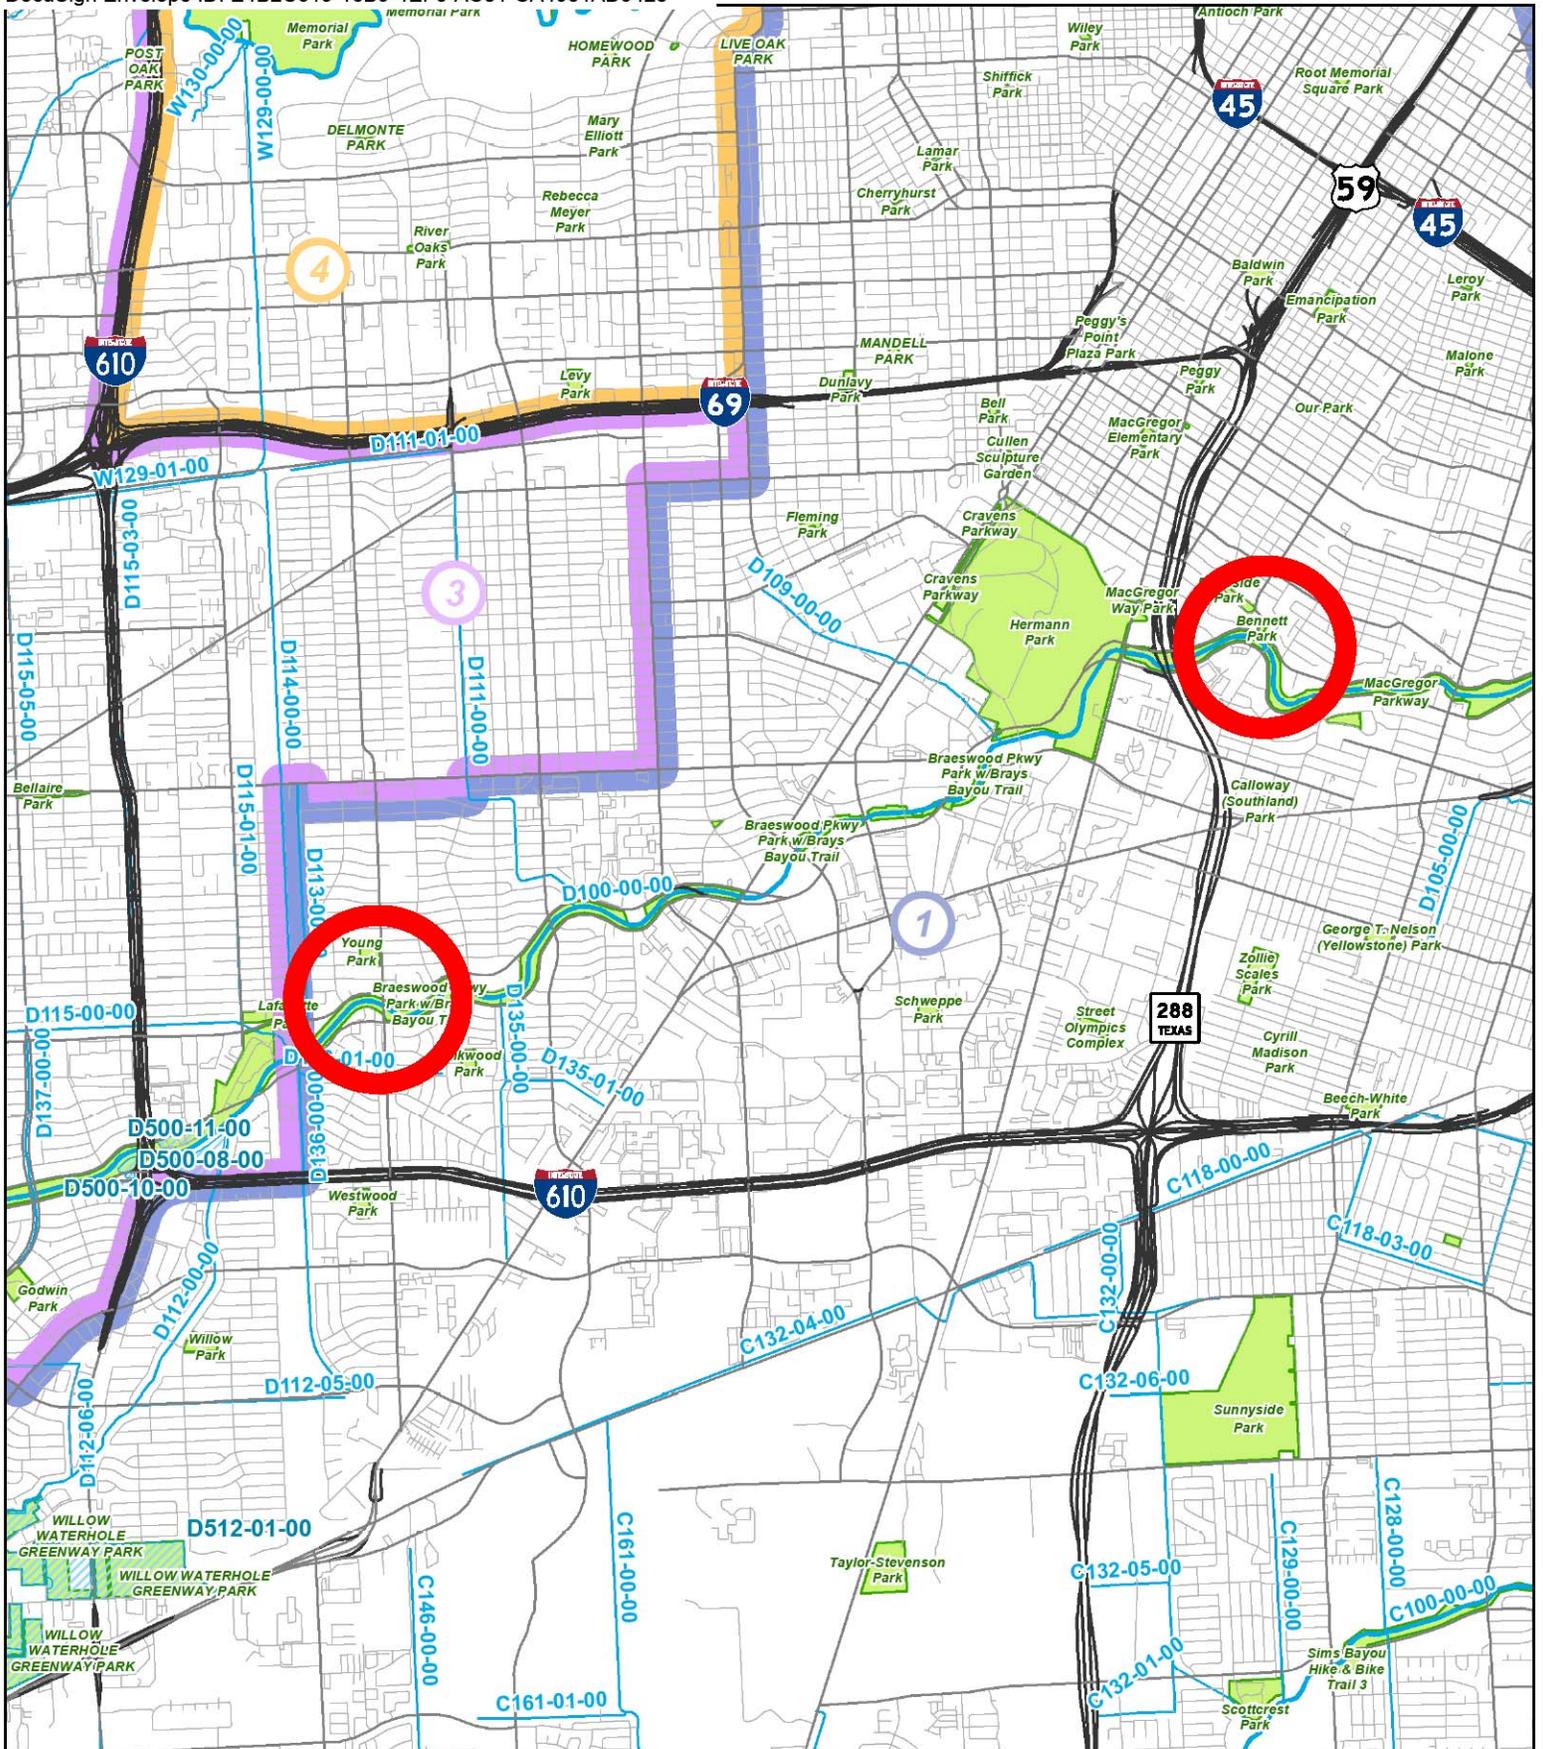

Project ID: D100-00-00-B027
Watershed: Brays Bayou
Precinct: 1

Pct No

- 1
- 2
- 3
- 4

