

Job Number: 19/0360
Record No.: CC-0003

CHANGE IN CONTRACT

Harris County Flood Control District

Contractor:	SPRINT SAND & CLAY LLC	Date:	10/13/2021
Address:	2141 PRESTON ST	PO Number:	P0000000327
	RICHMOND, TX	PS Fund:	
	77469-1418	PS Activity:	
Project Name:	South Belt Stormwater Detention Basin Excavation, Phase 3		
Project ID:	A520-03-00-E003		

Contractor: In connection with your contract dated 1/28/2020, for construction of the above mentioned job, the work or material outlined below was not comprehended in the original contract, or the following deduction is desired. When this order has been properly filled in, and approved, please proceed to do this work in accordance with the alterations set out below:

Description of Change Desired




The purpose of this change is to increase contract time in accordance with inclement weather provisions for weather days experienced from 4/20/20 to 9/15/21.


The number of inclement weather days has exceeded 110% of the provided 80 weather days included in the contract.
Total approved weather days from 4/20/20 to 9/15/21 = 154 days.
(154 days approved) - (80 days included in contract) = 74 days to be added to the contract for inclement weather.

This change results in no change to the contract value and adds a total of 74 days to the contract for inclement weather.

Estimate of Cost

Change Type	Pay Item ID	Pay Item Name	Unit	Quantity	Unit Price	Amount
Decrease						
	Subtotal					0.00
Increase						
	Subtotal					0.00
Addition						
	Subtotal					0.00
		Changes in Calendar days: 74				

	TOTAL ADDED TO CONTRACT:	0.00
	TOTAL DEDUCTED FROM CONTRACT:	0.00
	NET CHANGE:	0.00
If applicable, the Auditor's certification is made when the purchase order is amended in the system.	Approved:  <small>DocuSigned by: 15515E0D5700454...</small>	
	Print Name: <u>Gene Rushing</u> Project Manager	
Basis and Work Agreeable to Us.	Approved:  <small>DocuSigned by: 2E085FDADEC4476...</small>	
	Print Name: <u>Alan Black</u> HCFC, Executive Director	
Contractor: SPRINT SAND & CLAY LLC		
Signed:  <small>DocuSigned by: E6951BC7F137200...</small>		
Print Name: <u>Jacob Phillips</u> For the Contractor		
	Authorized in Minutes Of: _____	

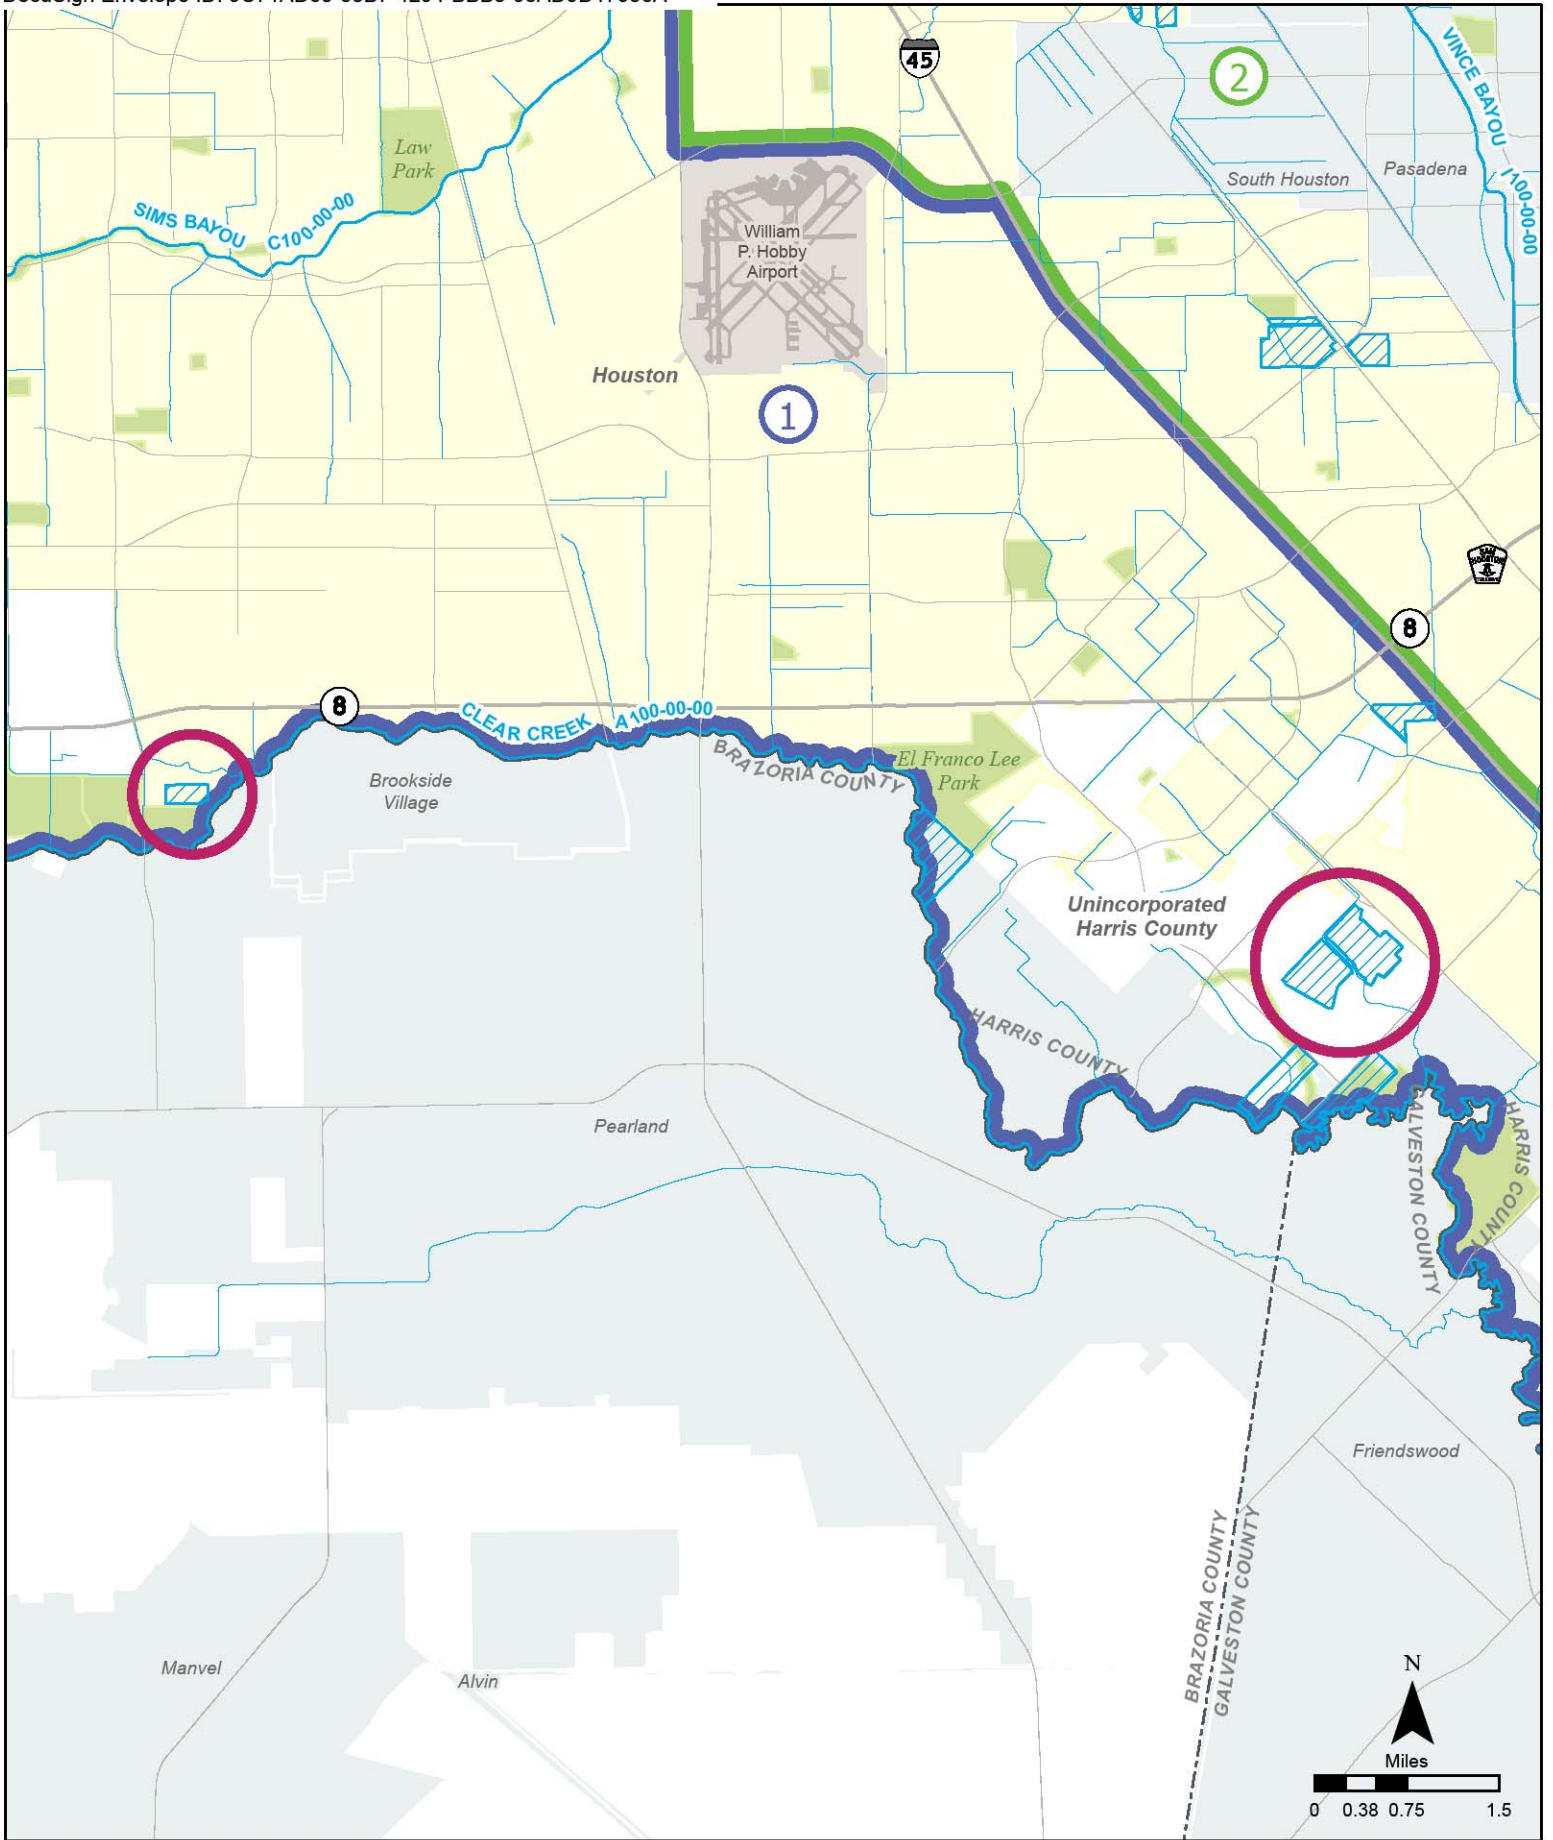

Project ID: A520-03-00-E003

Watershed: Clear Creek
Precinct: 1

