

Job Number: 19/0365
Record No.: CC-0016

CHANGE IN CONTRACT

Harris County Flood Control District

Contractor:	JAMES CONSTRUCTION GROUP LLC	Date:	8/16/2022			
Address:	222 PENNBRIGHT DR	PO Number:	P0000000841			
	HOUSTON, TX	PS Fund:				
	770905921	PS Activity:				
Project Name:	Brays Bayou Federal Flood Control Project					
Project ID:	D100-00-00-B047					
<p><i>Contractor: In connection with your contract dated 2/25/2020, for construction of the above mentioned job, the work or material outlined below was not comprehended in the original contract, or the following deduction is desired. When this order has been properly filled in, and approved, please proceed to do this work in accordance with the alterations set out below:</i></p>						
Description of Change Desired						
<p>This Contract Change is to add 72 days to the contract time because the Start date for the work at Calhoun has been delayed by the TXDOT Calhoun bridge project from July 1, 2022 to September 12, 2022. Previous contract change added 184 days to the contract time because TXDOT's projected completion date for their bridge project was June 30, 2022. The 184 days extended the completion date for this project to September 30, 2022 to provide 3 months of construction time for James Construction to perform the work at the Calhoun site. TXDOT has changed their projected completion date to September 11, 2022. This change extends the contract time to December 11, 2022 to provide James Construction 90 days to perform the work - from September 12, 2022 to December 11, 2022.</p>						
Estimate of Cost						
Change Type	Pay Item ID	Pay Item Name	Unit	Quantity	Unit Price	Amount
Decrease						
			Subtotal			
Increase						
			Subtotal			
Addition						
			Subtotal			
		Changes in Calendar days:	72			

If applicable, the Auditor's certification is made when the purchase order is amended in the system.

TOTAL ADDED TO CONTRACT: 0.00

TOTAL DEDUCTED FROM CONTRACT: 0.00

NET CHANGE: 0.00

DocuSigned by:
Approved: Mike Salch
6E18DACE17E44AD...

Print Name: Mike Salch
Project Manager

Basis and Work Agreeable to Us.

DocuSigned by:
Approved: Tina Petersen
2B80E09B0F95484...


Print Name: Tina Petersen
HCFCF, Executive Director

Contractor: JAMES CONSTRUCTION GROUP LLC

Signed: Rik van den Berg
C95C5A2879624E1...
For the Contractor

Print Name: Rik van den Berg

Authorized in Minutes Of: _____

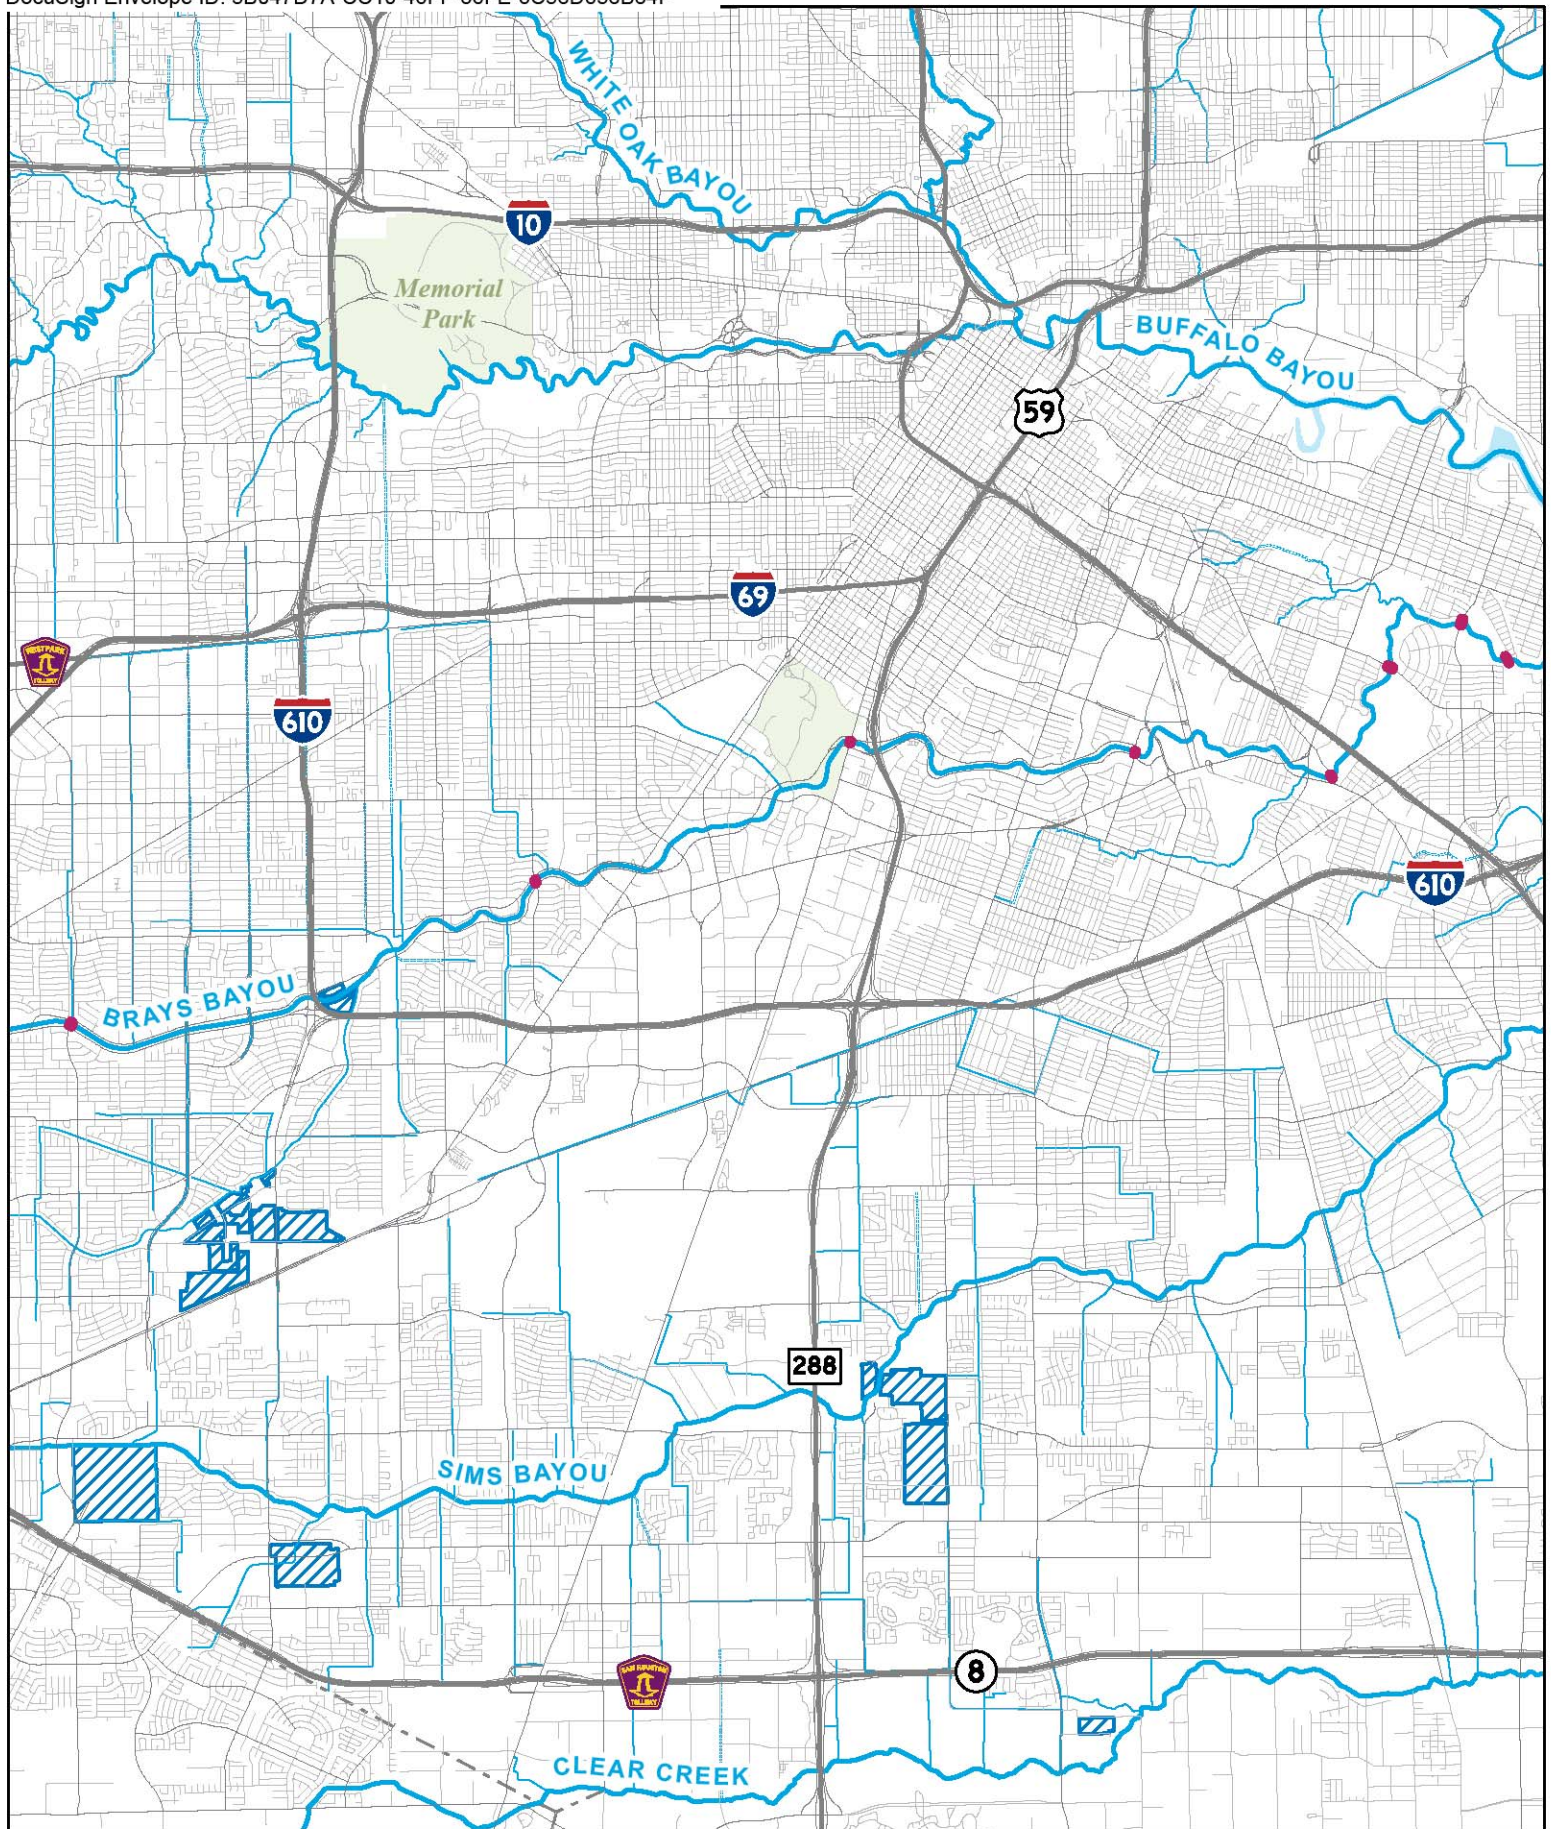

Project ID: D100-00-00-B047
Watershed: Brays Bayou
Precinct: 1, 2, 4

- Harris County Precincts**
 Judge Lina Hidalgo
- 1 - Rodney Ellis
 - 2 - Adrian Garcia
 - 3 - Tom S. Ramsey, P.E.
 - 4 - R. Jack Cagle

