

Job Number: 20/0347
Record No.: CC-0010**CHANGE IN CONTRACT**

Harris County Flood Control District

Contractor:	RAGLE INC	Date:	8/18/2022			
Address:	PO BOX 1130	PO Number:	P0000001588			
	EULESS, TX	PS Fund:				
	76039	PS Activity:				
Project Name:	South Rice Ave and Chimney Rock Bridges					
Project ID:	D100-00-00-B030					
<i>Contractor: In connection with your contract dated 12/15/2020, for construction of the above mentioned job, the work or material outlined below was not comprehended in the original contract, or the following deduction is desired. When this order has been properly filled in, and approved, please proceed to do this work in accordance with the alterations set out below:</i>						
Description of Change Desired						
<p>This Contract Change is to add a new pay item and to add days to the contract time due to inclement weather. A Pay Item is being added to provide a method for compensating the Contractor for the construction of METRO bus pads which were added to the project. 5 days are added to the contract due to inclement weather which impacted the completion time of the project for the period of time between April 16, 2022 and May 15, 2022. The number of inclement weather days stipulated in the contract was previously exceeded. CC-0006 added 40 days and CC-008 added 15 days to the contract for inclement weather days prior to April 16, 2022.</p> <p>The cost increase due to the addition of the bus pads is being offset by a decrease Channel Lining (8 inch), which we have determined will underrun the contract quantity.</p>						
Estimate of Cost						
Change Type	Pay Item ID	Pay Item Name	Unit	Quantity	Unit Price	Amount
Decrease	02376-04	CONCRETE CHANNEL LINING, 8 NOMINAL THICKNESS	SY	-151.12	165.00	-24,935.30
					Subtotal	-24,935.30
Increase						
					Subtotal	0.00
Addition	02875-01	RELOCATE BUS SHELTER	LS	2.00	4,987.06	9,974.12
	02875-01	RELOCATE BUS SHELTER	LS	3.00	4,987.06	14,961.18
					Subtotal	24,935.30
		Changes in Calendar days: 5				

TOTAL ADDED TO CONTRACT: 24,935.30

TOTAL DEDUCTED FROM CONTRACT: -24,935.30

NET CHANGE: 0.00

If applicable, the Auditor's certification is made when the purchase order is amended in the system.

DocuSigned by:
Approved: Mike Salch
6E18DACE17E44AD...

Print Name: Mike Salch
Project Manager

Basis and Work Agreeable to Us.

DocuSigned by:
Approved: Tina Petersen
2B86E69B8F95484...


Print Name: Tina Petersen
HCFCD, Executive Director

Contractor: RAGLE INC

Signed: David Griffin
B7A25EA2A3E7A354
For the Contractor

Print Name: David Griffin

Authorized in Minutes Of: _____

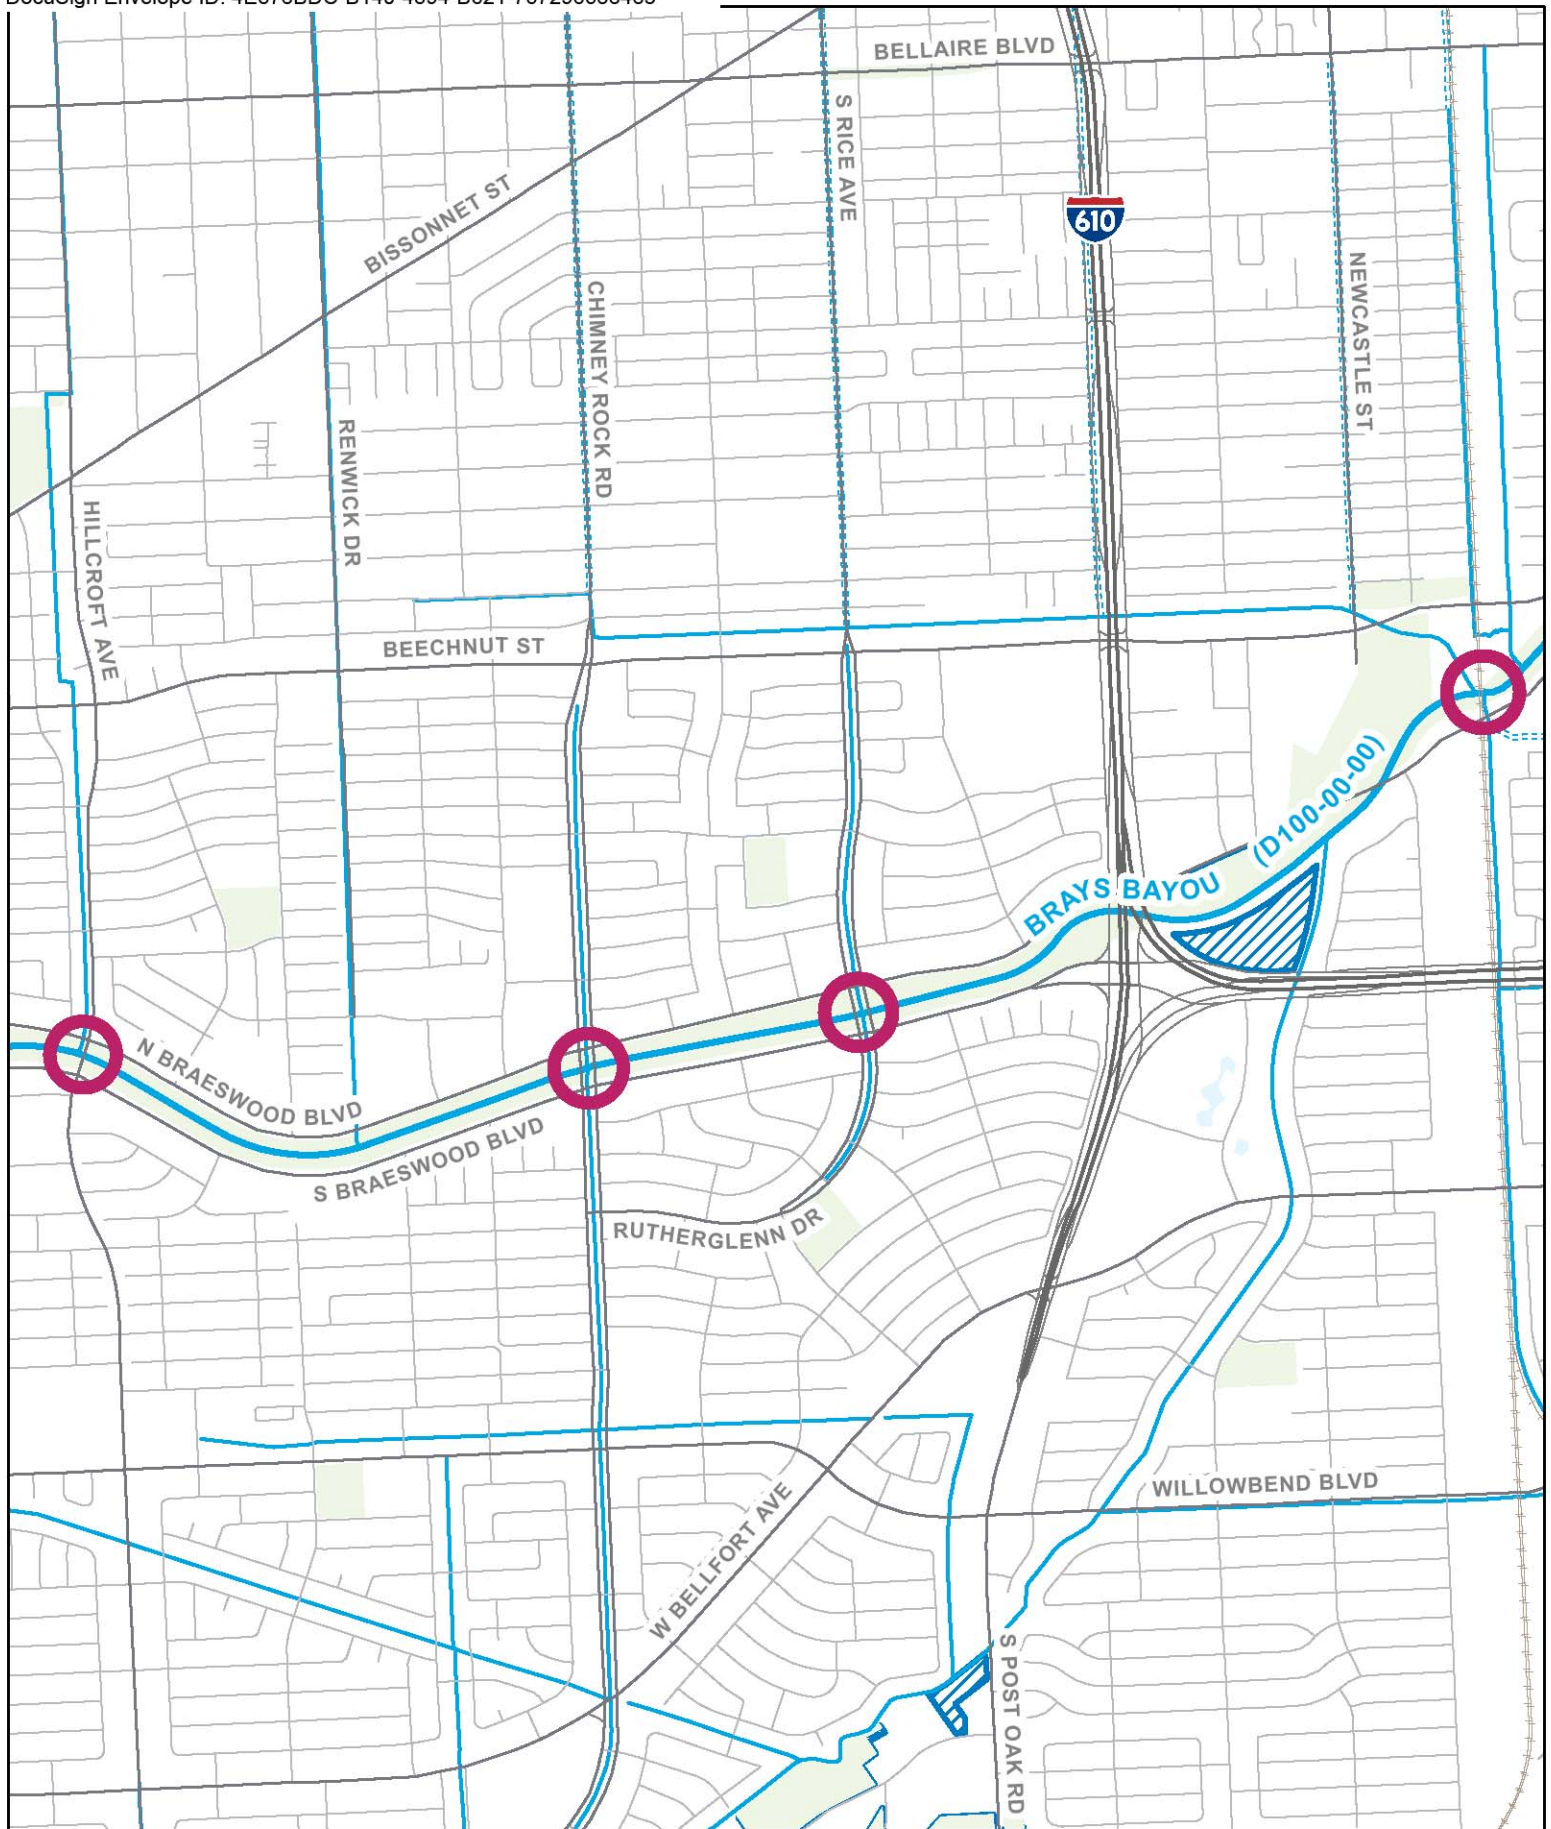

Project ID: D100-00-00-B030

Watershed: Brays Bayou

Precinct: 1, 4

- Project Boundary
- Harris County Precincts**
Judge Lina Hidalgo
- 1 - Rodney Ellis
 - 2 - Adrian Garcia
 - 3 - Tom S. Ramsey, P.E.
 - 4 - R. Jack Cagle

