

Job Number: 20/0106  
Record No.: CC-0004**CHANGE IN CONTRACT****Harris County Flood Control District**

Contractor:	SER CONSTRUCTION PARTNERS LLC	Date:	8/12/2022			
Address:	3636 PASADENA BLVD	PO Number:	P0000001331			
	PASADENA, TX	PS Fund:				
	77503-3208	PS Activity:				
Project Name:	Widening and Deepening of Armand Bayou at Sam Houston Tollway East					
Project ID:	B100-00-00-E002					
<p>Contractor: In connection with your contract dated 7/28/2020, for construction of the above mentioned job, the work or material outlined below was not comprehended in the original contract, or the following deduction is desired. When this order has been properly filled in, and approved, please proceed to do this work in accordance with the alterations set out below:</p>						
<b>Description of Change Desired</b>						
<p>The purpose of this change is to reconcile final quantities for final payment. This change includes extension of quantities for final surveyed excavation as well as several items added to the scope of work. Remaining quantity balances of several pay items are being deducted to offset the proposed increases.</p> <p>Final surveyed earthwork quantities exceeded available contract quantities due to lack of original survey detail under Beltway 8. Traffic delineators are added to mark the ends of Beltway sidewalks at the bayou for safety, a Type A Inlet and culverts were added to improve a steep road ditch condition, a sewer reconnection was added for a service line encountered when constructing the new storm outfall on Oleander Street, quantity for Concrete Driveways and sodding is extended where the actual quantity required was more than anticipated.</p>						
<b>Estimate of Cost</b>						
Change Type	Pay Item ID	Pay Item Name	Unit	Quantity	Unit Price	Amount
<b>Decrease</b>	02120-03	REMOVE & DISPOSE OF CONCRETE RUBBLE AND CONCRETE STRUCTURES	CY	-1,610.00	16.00	-25,760.00
	01562-01	CONSTRUCTION FENCE	LF	-5,100.00	3.00	-15,300.00
	02120-04	REMOVE & DISPOSE OF ALL PIPE	LF	-2,050.00	18.00	-36,900.00
	02120-20	EXCAVATION, REMOVAL & DISPOSAL OF IMPACTED SOIL	CY	-173.23	55.00	-9,527.58
	02376-02	CONCRETE CHANNEL LINING, 5 NOMINAL THICKNESS	SY	-544.00	100.00	-54,400.00
					<b>Subtotal</b>	-141,887.58
<b>Increase</b>	02632-01	TYPE A INLET	EA	1.00	1,941.00	1,941.00
	02611-02	24-INCH REINFORCED CONCRETE PIPE	LF	16.00	139.00	2,224.00
	02315-02	EXCAVATION & OFF-SITE DISPOSAL	CY	6,500.00	17.00	110,500.00
	02315-03	EXCAVATION & FILL (ON-SITE MATERIAL)	CY	2,326.00	10.00	23,260.00
	02120-03	REMOVE & DISPOSE OF CONCRETE RUBBLE AND CONCRETE STRUCTURES	CY	10.00	16.00	160.00
	02754-01	CONCRETE DRIVEWAY	SY	3.00	88.00	264.00
	02921-16	ANCHORED SODDING	SY	28.39	9.60	272.54
	01555-01	TRAFFIC CONTROL	LS	0.01	88,320.00	1,020.00
	02534-02	SANITARY SEWER SERVICE RECONNECTION WITH OR WITHOUT STACK	EA	1.00	2,246.04	2,246.04

County Auditor's Form 1258  
Harris County TX (REV. 5/17/2017)

Addition					
		Subtotal			141,887.58
		Subtotal			0.00
	Changes in Calendar days: 0				


TOTAL ADDED TO CONTRACT:	141,887.58
TOTAL DEDUCTED FROM CONTRACT:	-141,887.58
NET CHANGE:	0.00

If applicable, the Auditor's certification is made when the purchase order is amended in the system.

DocuSigned by:  
Approved:   
15515E6B3760454...

Print Name: Gene Rushing  
Project Manager

Basis and Work Agreeable to Us.

DocuSigned by:  
Approved:   
2B86EC9B8F95484...


Print Name: Tina Petersen  
HCFCD, Executive Director

Contractor: SER CONSTRUCTION PARTNERS LLC

Signed:   
0DF8502CE90A46D...  
For the Contractor

Print Name: Eddie Ramos

Authorized in Minutes Of: \_\_\_\_\_

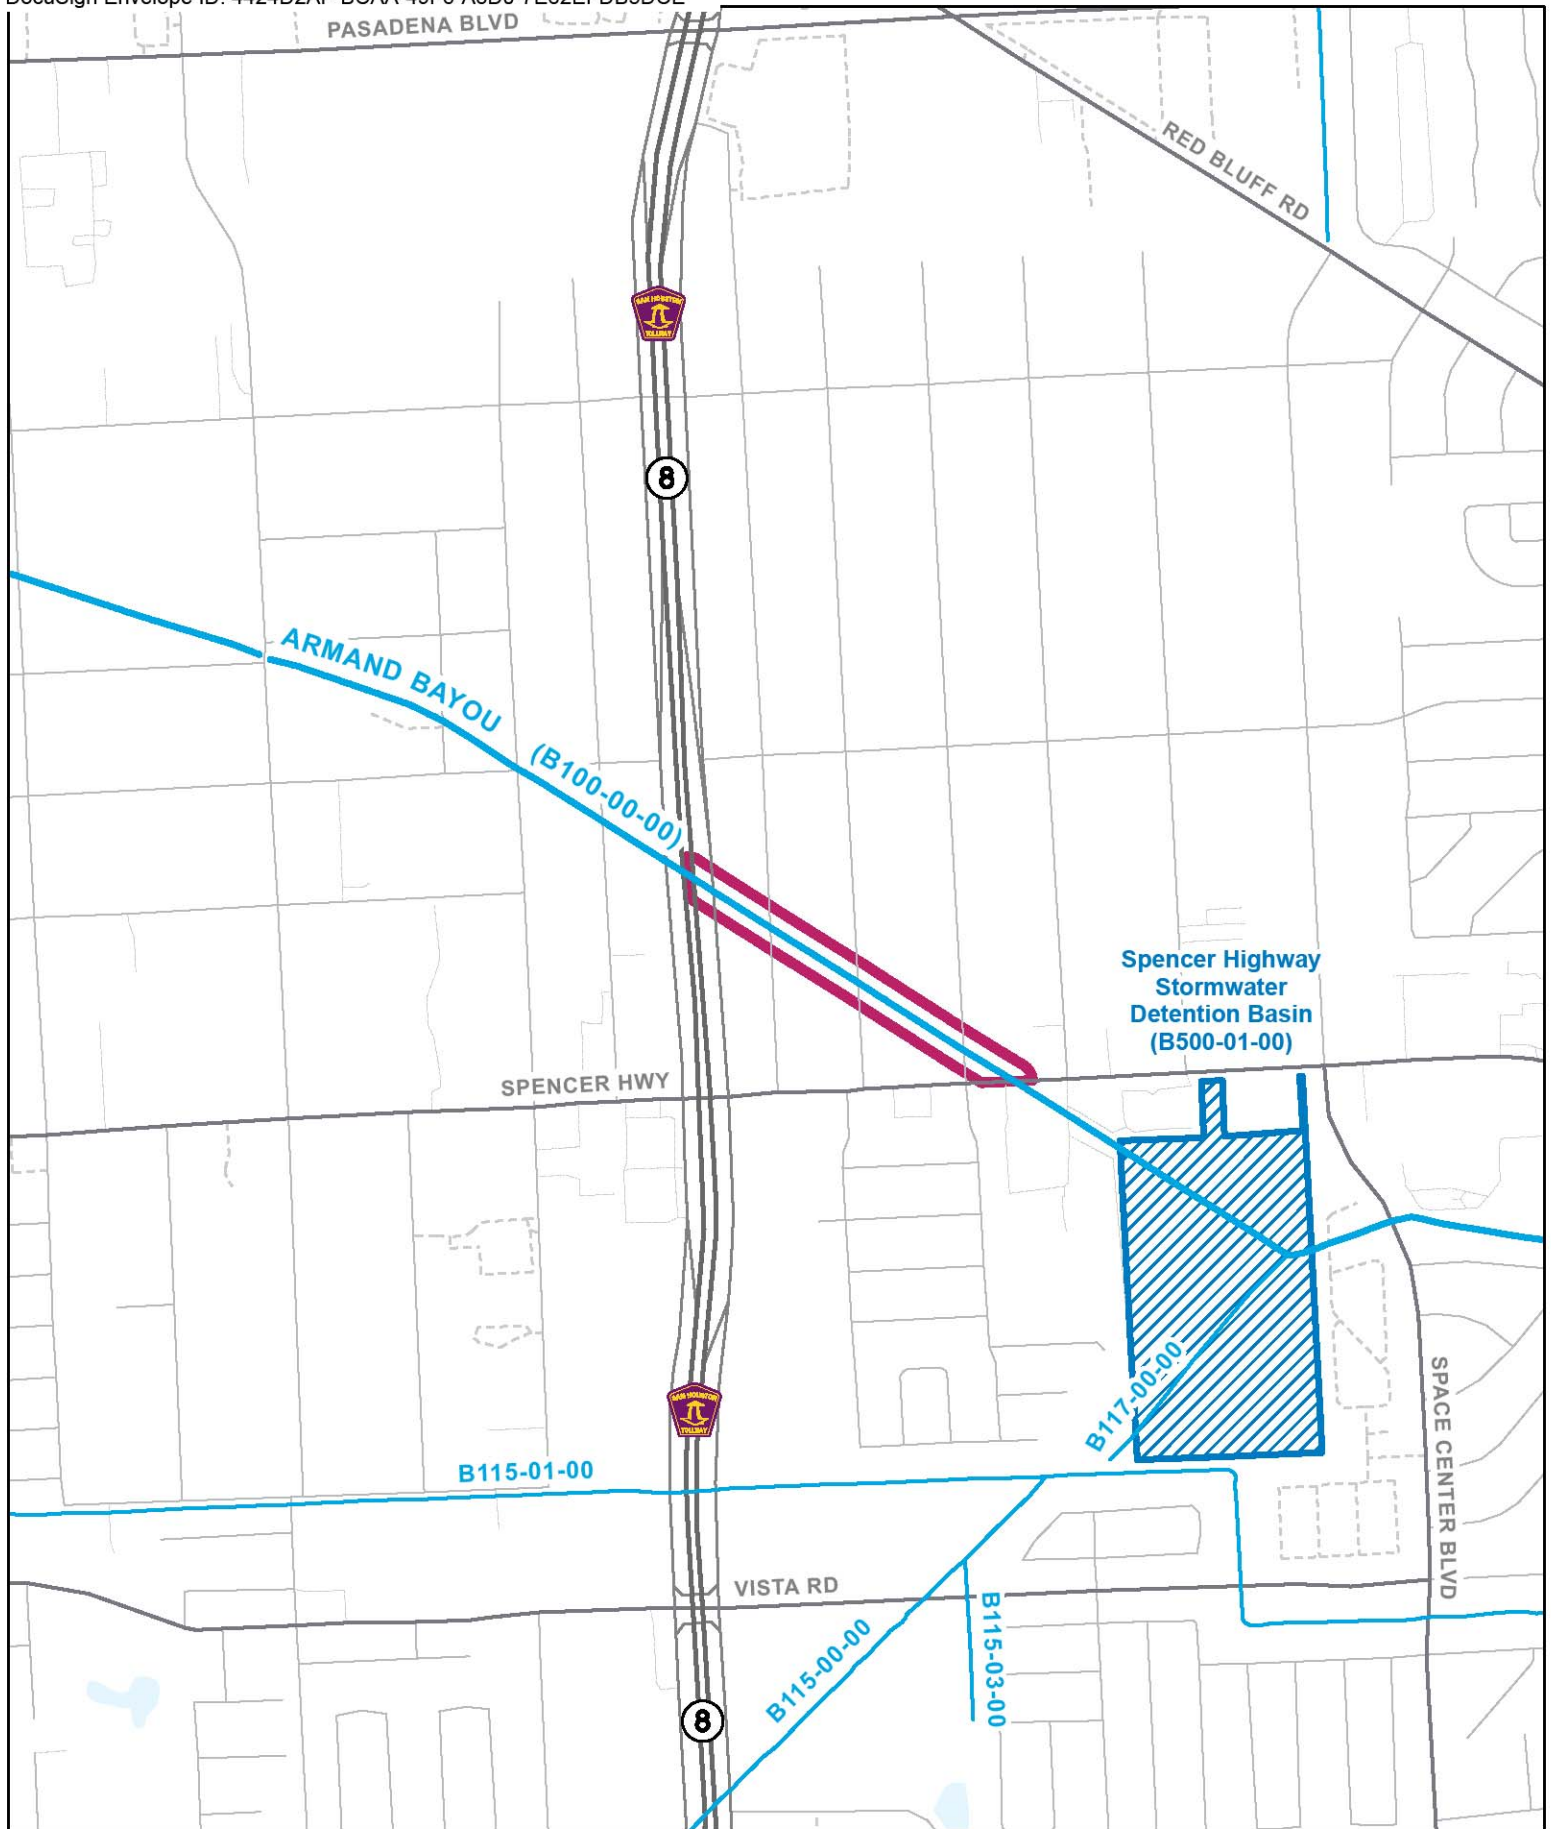

**Project ID: B100-00-00-E002**

**Watershed: Armand Bayou**

**Precinct: 2**

- Project Boundary
- Harris County Precincts**  
Judge Lina Hidalgo
- 1 - Rodney Ellis
  - 2 - Adrian Garcia
  - 3 - Tom S. Ramsey, P.E.
  - 4 - R. Jack Cagle

