

Job Number: 22/0085
Record No.: CC-0006**CHANGE IN CONTRACT**

Harris County Flood Control District


Contractor: LECON INC		Date: 2/27/2024				
Address:		PO Number:				
		PS Fund:				
		PS Activity:				
Project Name: Major Maintenance of Cypress Creek and Tributaries Batch 3						
Project ID: K100-00-00-X087						
<i>Contractor: In connection with your contract dated 5/10/2022, for construction of the above mentioned job, the work or material outlined below was not comprehended in the original contract, or the following deduction is desired. When this order has been properly filled in, and approved, please proceed to do this work in accordance with the alterations set out below:</i>						
Description of Change Desired						
This Change in Contract reconciles quantities across eight sites and extends the time of completion due to inclement weather. Cost increases from quantity adjustments are balanced by deducting unused plan quantities not needed for completion, resulting in no net change in the contract value. 1. Changes to Sites K111-02-00-X006 and K111-02-01-X003 include replacing additional corrugated metal pipes (CMP's), adding backslope swales and interceptors, and adjusting earthwork quantities based on the final survey. (Refer to PCC-0022 & PCC-0034) 2. Changes to Site K112-00-00-X006 include adjusting earthwork quantities based on the final survey and deducting unused plan quantities not needed for completion. (Refer to PCC-0026 & PCC-0036) 3. Changes to Site K112-01-00-X008 include adjusting earthwork quantities based on the final survey, increasing insufficient plan quantities, and deducting unused plan quantities that are not needed for completion. (Refer to PCC-0030 & PCC-0037) 4. Changes to Site K120-00-00-X026 include increasing insufficient plan quantities and deducting unused plan quantities that are not needed for completion. (Refer to PCC-0032) 5. Changes to Site K120-03-00-X008 include deducting unused plan quantities that are not needed for completion. (Refer to PCC-0038) 6. Changes to Site K124-02-00-X020 include: - Reduction in scope due to site access limitations (Refer to PCC-0021) - Reduction in earthwork cost due to suitability of on-site material in-lieu of import fill (Refer to PCC-0023) - Increases due to Pre-Construction Survey: Earthwork, 3x5 Granular Fill and Grade 1 Riprap (Refer to PCC-0028) - Additional repairs: Increases to Grade 1 Riprap, CMP's and interceptors (Refer to PCC-0033) - Changes to Concrete Headwalls and CMP's: additional quantities and pipe size change (Refer to PCC-0035) 7. Changes to Site K145-00-00-X019 include adjusting earthwork quantities based on the final survey, increasing insufficient plan quantities, and deducting unused plan quantities that are not needed for completion. (Refer to PCC-0024 & PCC-0031) 8. Extension of Time due to Inclement Weather: Additional 30-days As of January 31, 2024, the Contractor has experienced a total of 109-days of inclement weather which have impacted the critical path. The contract provides for 79-days of inclement weather, and the 110% threshold for additional time due to inclement weather has been exceeded. (Refer to PCC-0027, PCC-0029, PCC-0039)						
Estimate of Cost						
Change Type	Pay Item ID	Pay Item Name	Unit	Quantity	Unit Price	Amount
Decrease						
	02315-02	EXCAVATION & OFF-SITE DISPOSAL	CY	-281.94	22.50	-6,343.75
	02315-01	EXCAVATION & REMOVAL, DRAINAGE/DRYING AND DISPOSAL IN A LANDFILL	CY	-470.00	35.00	-16,450.00
	02315-02	EXCAVATION & OFF-SITE DISPOSAL	CY	-3,824.00	22.50	-86,040.00
	02642-02	24-INCH CORRUGATED METAL PIPE	LF	-6.00	130.00	-780.00
	02315-02	EXCAVATION & OFF-SITE DISPOSAL	CY	-1,402.00	22.50	-31,545.00
	01562-01	CONSTRUCTION FENCE	LF	-387.00	4.00	-1,548.00
	02120-02	DEBRIS AND TRASH REMOVAL AND DISPOSAL IN A LANDFILL	CY	-50.00	55.00	-2,750.00
	02120-09	REMOVE & DISPOSE OF TIRES <= 16	EA	-10.00	105.00	-1,050.00

02120-10	REMOVE & DISPOSE OF TIRES >16	EA	-10.00	110.00	-1,100.00
02120-33	DISMOUNT RIM (IF ATTACHED TO TIRE), ALL DIAMETERS	EA	-5.00	50.00	-250.00
02269-01	TRENCH SHORING SYSTEM,5 TO 20 FEET	LF	-17.00	15.00	-255.00
02315-01	EXCAVATION & REMOVAL,DRAINAGE/DRYING AND DISPOSAL IN A LANDFILL	CY	-246.00	35.00	-8,610.00
02365-01	STABILIZED CONSTRUCTION ACCESS	SY	-1.78	35.00	-62.30
02376-06	CONCRETE INTERCEPTOR STRUCTURE	SY	-1.24	190.00	-235.60
02611-05	42-INCH REINFORCED CONCRETE PIPE	LF	-5.00	340.00	-1,700.00
02315-02	EXCAVATION & OFF-SITE DISPOSAL	CY	-1,290.00	22.50	-29,025.00
02315-04	IMPORTED FILL	CY	-1,801.00	27.00	-48,627.00
02315-04	IMPORTED FILL	CY	-299.00	27.00	-8,073.00
02315-02	EXCAVATION & OFF-SITE DISPOSAL	CY	-157.00	22.50	-3,532.50
02642-06	48-INCH CORRUGATED METAL PIPE	LF	-92.00	240.00	-22,080.00
02464-01	HCFC D TIMBER BENT FOR PIPE OUTFALLS	EA	-1.00	2,500.00	-2,500.00
02315-01	EXCAVATION & REMOVAL,DRAINAGE/DRYING AND DISPOSAL IN A LANDFILL	CY	-17.00	35.00	-595.00
02642-08	60-INCH CORRUGATED METAL PIPE	LF	-106.00	330.00	-34,980.00
02315-02	EXCAVATION & OFF-SITE DISPOSAL	CY	-285.00	22.50	-6,412.50
02315-04	IMPORTED FILL	CY	-1,500.00	27.00	-40,500.00
02315-01	EXCAVATION & REMOVAL,DRAINAGE/DRYING AND DISPOSAL IN A LANDFILL	CY	-562.00	35.00	-19,670.00
02315-04	IMPORTED FILL	CY	-378.00	27.00	-10,206.00
02315-01	EXCAVATION & REMOVAL,DRAINAGE/DRYING AND DISPOSAL IN A LANDFILL	CY	-99.00	35.00	-3,465.00
02315-02	EXCAVATION & OFF-SITE DISPOSAL	CY	-6,371.00	22.50	-143,347.50
01562-01	CONSTRUCTION FENCE	LF	-1,000.00	4.00	-4,000.00
01566-08	TREE ROOT PRUNING	LF	-1,847.84	20.00	-36,956.70
01566-11	TREE PROTECTION FENCING (CHAIN LINK)	LF	-2,150.00	9.00	-19,350.00
02120-02	DEBRIS AND TRASH REMOVAL AND DISPOSAL IN A LANDFILL	CY	-14.58	55.00	-801.90
02120-04	REMOVE & DISPOSE OF ALL PIPE	LF	-4.00	10.00	-40.00
02120-10	REMOVE & DISPOSE OF TIRES >16	EA	-15.00	110.00	-1,650.00
02120-33	DISMOUNT RIM (IF ATTACHED TO TIRE), ALL DIAMETERS	EA	-9.00	50.00	-450.00
02269-01	TRENCH SHORING SYSTEM,5 TO 20 FEET	LF	-166.00	15.00	-2,490.00
02315-06	BACKSLOPE DRAINAGE SYSTEM SWALES	LF	-283.00	3.80	-1,075.40
02361-02	REINFORCED SILT FENCE	LF	-450.00	3.00	-1,350.00
02364-02	FILTER DAM - TYPE 2	LF	-40.00	120.00	-4,800.00
02365-01	STABILIZED CONSTRUCTION ACCESS	SY	-1.78	35.00	-62.30
02378-06	GRANULAR FILL, 3-5 INCHES	TON	-47.61	59.00	-2,808.99
02378-22	RIPRAP,GRADATION NO. 1	TON	-773.30	80.00	-61,864.00
02378-23	RIPRAP,GRADATION NO. 2	TON	-247.06	81.00	-20,011.86
02611-10	72-INCH REINFORCED CONCRETE PIPE	LF	-5.00	750.00	-3,750.00
02642-02	24-INCH CORRUGATED METAL PIPE	LF	-42.00	130.00	-5,460.00
02642-03	30-INCH CORRUGATED METAL PIPE	LF	-10.00	150.00	-1,500.00
02642-04	36-INCH CORRUGATED METAL PIPE	LF	-17.00	175.00	-2,975.00
02642-08	60-INCH CORRUGATED METAL PIPE	LF	-25.00	330.00	-8,250.00
02921-16	ANCHORED SODDING	SY	-381.88	6.00	-2,291.28
01562-01	CONSTRUCTION FENCE	LF	-150.00	4.00	-600.00
01566-08	TREE ROOT PRUNING	LF	-1,350.00	20.00	-27,000.00
01566-11	TREE PROTECTION FENCING (CHAIN LINK)	LF	-1,050.00	9.00	-9,450.00
02120-04	REMOVE & DISPOSE OF ALL PIPE	LF	-53.00	10.00	-530.00
02120-09	REMOVE & DISPOSE OF TIRES <= 16	EA	-19.00	105.00	-1,995.00
02120-10	REMOVE & DISPOSE OF TIRES >16	EA	-8.00	110.00	-880.00
02120-33	DISMOUNT RIM (IF ATTACHED TO TIRE), ALL DIAMETERS	EA	-5.00	50.00	-250.00
02269-01	TRENCH SHORING SYSTEM,5 TO 20 FEET	LF	-119.88	15.00	-1,798.20

	02315-06	BACKSLOPE DRAINAGE SYSTEM SWALES	LF	-1,221.00	3.80	-4,639.80
	02361-02	REINFORCED SILT FENCE	LF	-305.00	3.00	-915.00
	02364-02	FILTER DAM - TYPE 2	LF	-10.00	120.00	-1,200.00
	02365-01	STABILIZED CONSTRUCTION ACCESS	SY	-1.78	35.00	-62.30
	02378-06	GRANULAR FILL, 3-5 INCHES	TON	-593.84	59.00	-35,036.56
	02378-22	RIPRAP, GRADATION NO. 1	TON	-372.21	80.00	-29,776.80
	02630-01	TYPE C MANHOLE, FOR 42 AND SMALLER	EA	-1.00	10,000.00	-10,000.00
	02642-02	24-INCH CORRUGATED METAL PIPE	LF	-56.00	130.00	-7,280.00
	02642-04	36-INCH CORRUGATED METAL PIPE	LF	-22.00	175.00	-3,850.00
	02921-16	ANCHORED SODDING	SY	-257.80	6.00	-1,546.80
	02120-09	REMOVE & DISPOSE OF TIRES <= 16	EA	-20.00	105.00	-2,100.00
	02120-10	REMOVE & DISPOSE OF TIRES >16	EA	-10.00	110.00	-1,100.00
	02120-33	DISMOUNT RIM (IF ATTACHED TO TIRE), ALL DIAMETERS	EA	-30.00	50.00	-1,500.00
	02269-01	TRENCH SHORING SYSTEM, 5 TO 20 FEET	LF	-237.00	15.00	-3,555.00
	02315-06	BACKSLOPE DRAINAGE SYSTEM SWALES	LF	-684.00	3.80	-2,599.20
	02322-01	FLOWABLE CONCRETE FILL	CY	-50.00	220.00	-11,000.00
	02361-02	REINFORCED SILT FENCE	LF	-256.00	3.00	-768.00
	02364-02	FILTER DAM - TYPE 2	LF	-99.00	120.00	-11,880.00
	02365-01	STABILIZED CONSTRUCTION ACCESS	SY	-225.78	35.00	-7,902.30
	02376-06	CONCRETE INTERCEPTOR STRUCTURE	SY	-22.73	190.00	-4,318.70
	02378-05	GRANULAR FILL, GRAVEL TO RIPRAP GRADATION NO. 2, AS DIRECTED BY THE ENGINEER	TON	-162.09	75.00	-12,156.75
	02378-06	GRANULAR FILL, 3-5 INCHES	TON	-210.00	59.00	-12,390.00
	02378-22	RIPRAP, GRADATION NO. 1	TON	-107.20	80.00	-8,576.00
	02379-01	GEOTEXTILE FILTER MATERIAL FOR RIPRAP	SY	-80.25	4.00	-321.00
	02630-01	TYPE C MANHOLE, FOR 42 AND SMALLER	EA	-1.00	10,000.00	-10,000.00
	02642-02	24-INCH CORRUGATED METAL PIPE	LF	-54.00	130.00	-7,020.00
	02642-03	30-INCH CORRUGATED METAL PIPE	LF	-4.00	150.00	-600.00
	02642-04	36-INCH CORRUGATED METAL PIPE	LF	-10.00	175.00	-1,750.00
	02642-05	42-INCH CORRUGATED METAL PIPE	LF	-3.00	210.00	-630.00
	02642-08	60-INCH CORRUGATED METAL PIPE	LF	-19.00	330.00	-6,270.00
	02642-09	72-INCH CORRUGATED METAL PIPE	LF	-1.00	390.00	-390.00
	01562-01	CONSTRUCTION FENCE	LF	-2,520.00	4.00	-10,080.00
	01566-08	TREE ROOT PRUNING	LF	-825.00	20.00	-16,500.00
	01566-11	TREE PROTECTION FENCING (CHAIN LINK)	LF	-825.00	9.00	-7,425.00
	02120-02	DEBRIS AND TRASH REMOVAL AND DISPOSAL IN A LANDFILL	CY	-100.00	55.00	-5,500.00
	02120-03	REMOVE & DISPOSE OF CONCRETE RUBBLE AND CONCRETE STRUCTURES	CY	-8.02	38.00	-304.76
	02120-04	REMOVE & DISPOSE OF ALL PIPE	LF	-11.00	10.00	-110.00
Increase				Subtotal		-997,227.75
	02315-03	EXCAVATION & FILL (ON-SITE MATERIAL)	CY	1,500.00	16.00	24,000.00
	02315-03	EXCAVATION & FILL (ON-SITE MATERIAL)	CY	798.00	16.00	12,768.00
	02642-07	54-INCH CORRUGATED METAL PIPE	LF	99.00	300.00	29,700.00
	02642-04	36-INCH CORRUGATED METAL PIPE	LF	53.00	175.00	9,275.00
	02630-01	TYPE C MANHOLE, FOR 42 AND SMALLER	EA	1.00	10,000.00	10,000.00
	02378-22	RIPRAP, GRADATION NO. 1	TON	886.00	80.00	70,880.00
	02269-01	TRENCH SHORING SYSTEM, 5 TO 20 FEET	LF	75.00	15.00	1,125.00
	02632-05	URBAN INTERCEPTOR STRUCTURE	EA	2.00	5,500.00	11,000.00
	02642-02	24-INCH CORRUGATED METAL PIPE	LF	75.00	130.00	9,750.00
	02315-04	IMPORTED FILL	CY	3,627.00	27.00	97,929.00
	02642-03	30-INCH CORRUGATED METAL PIPE	LF	13.00	150.00	1,950.00
	02632-70	HEADWALLS AND WINGWALLS	CY	14.58	1,700.00	24,786.00
	02120-03	REMOVE & DISPOSE OF CONCRETE RUBBLE	CY	2.15	38.00	81.70

	AND CONCRETE STRUCTURES				
02315-03	EXCAVATION & FILL (ON-SITE MATERIAL)	CY	613.71	16.00	9,819.36
02120-04	REMOVE & DISPOSE OF ALL PIPE	LF	23.00	10.00	230.00
02269-01	TRENCH SHORING SYSTEM,5 TO 20 FEET	LF	64.00	15.00	960.00
02315-06	BACKSLOPE DRAINAGE SYSTEM SWALES	LF	958.00	3.80	3,640.40
02376-06	CONCRETE INTERCEPTOR STRUCTURE	SY	31.79	190.00	6,040.10
02642-02	24-INCH CORRUGATED METAL PIPE	LF	164.00	130.00	21,320.00
02120-04	REMOVE & DISPOSE OF ALL PIPE	LF	61.00	10.00	610.00
02315-01	EXCAVATION & REMOVAL,DRAINAGE/DRYING AND DISPOSAL IN A LANDFILL	CY	1,719.00	35.00	60,165.00
02315-02	EXCAVATION & OFF-SITE DISPOSAL	CY	203.00	22.50	4,567.50
02315-04	IMPORTED FILL	CY	4,965.00	27.00	134,055.00
02315-01	EXCAVATION & REMOVAL,DRAINAGE/DRYING AND DISPOSAL IN A LANDFILL	CY	66.00	35.00	2,310.00
02315-04	IMPORTED FILL	CY	1,097.00	27.00	29,619.00
02315-02	EXCAVATION & OFF-SITE DISPOSAL	CY	2,183.00	22.50	49,117.50
02378-06	GRANULAR FILL, 3-5 INCHES	TON	529.00	59.00	31,211.00
02378-22	RIPRAP,GRADATION NO. 1	TON	3,350.00	80.00	268,000.00
02315-04	IMPORTED FILL	CY	1,909.00	27.00	51,543.00
02120-03	REMOVE & DISPOSE OF CONCRETE RUBBLE AND CONCRETE STRUCTURES	CY	12.30	38.00	467.40
02120-02	DEBRIS AND TRASH REMOVAL AND DISPOSAL IN A LANDFILL	CY	88.67	55.00	4,876.85
02376-06	CONCRETE INTERCEPTOR STRUCTURE	SY	2.81	190.00	533.90
02376-03	CONCRETE CHANNEL LINING, 6 NOMINAL THICKNESS	SY	93.06	110.00	10,236.60
02378-23	RIPRAP,GRADATION NO. 2	TON	30.50	81.00	2,470.50
02921-16	ANCHORED SODDING	SY	101.32	6.00	607.92
02120-05	REMOVE & DISPOSE OF CONCRETE CHANNEL LINING	SY	93.06	17.00	1,582.02
Addition		Subtotal			997,227.75
		Subtotal			0.00
	Changes in Calendar days: 30				

	TOTAL ADDED TO CONTRACT:	997,227.75
	TOTAL DEDUCTED FROM CONTRACT:	-997,227.75
	NET CHANGE:	0.00
	If applicable, the Auditor's certification is made when the purchase order is amended in the system.	
Basis and Work Agreeable to Us.	Approved: DocuSigned by: <i>Zeke Saavedra</i> 6275655D0ACE4FC...	
	Print Name: Zeke Saavedra	
	Project Manager	
Contractor: LECON INC Signed: DocuSigned by: <i>David Hill</i> 4E445857A62E416... Full time Contractor Print Name: David Hill	Approved: DocuSigned by: <i>Tina Petersen</i> 2B86E69B8F95484...	
	Print Name: Tina Petersen	
	HCFCD, Executive Director	DS <i>JS</i>
	Authorized in Minutes Of: _____	

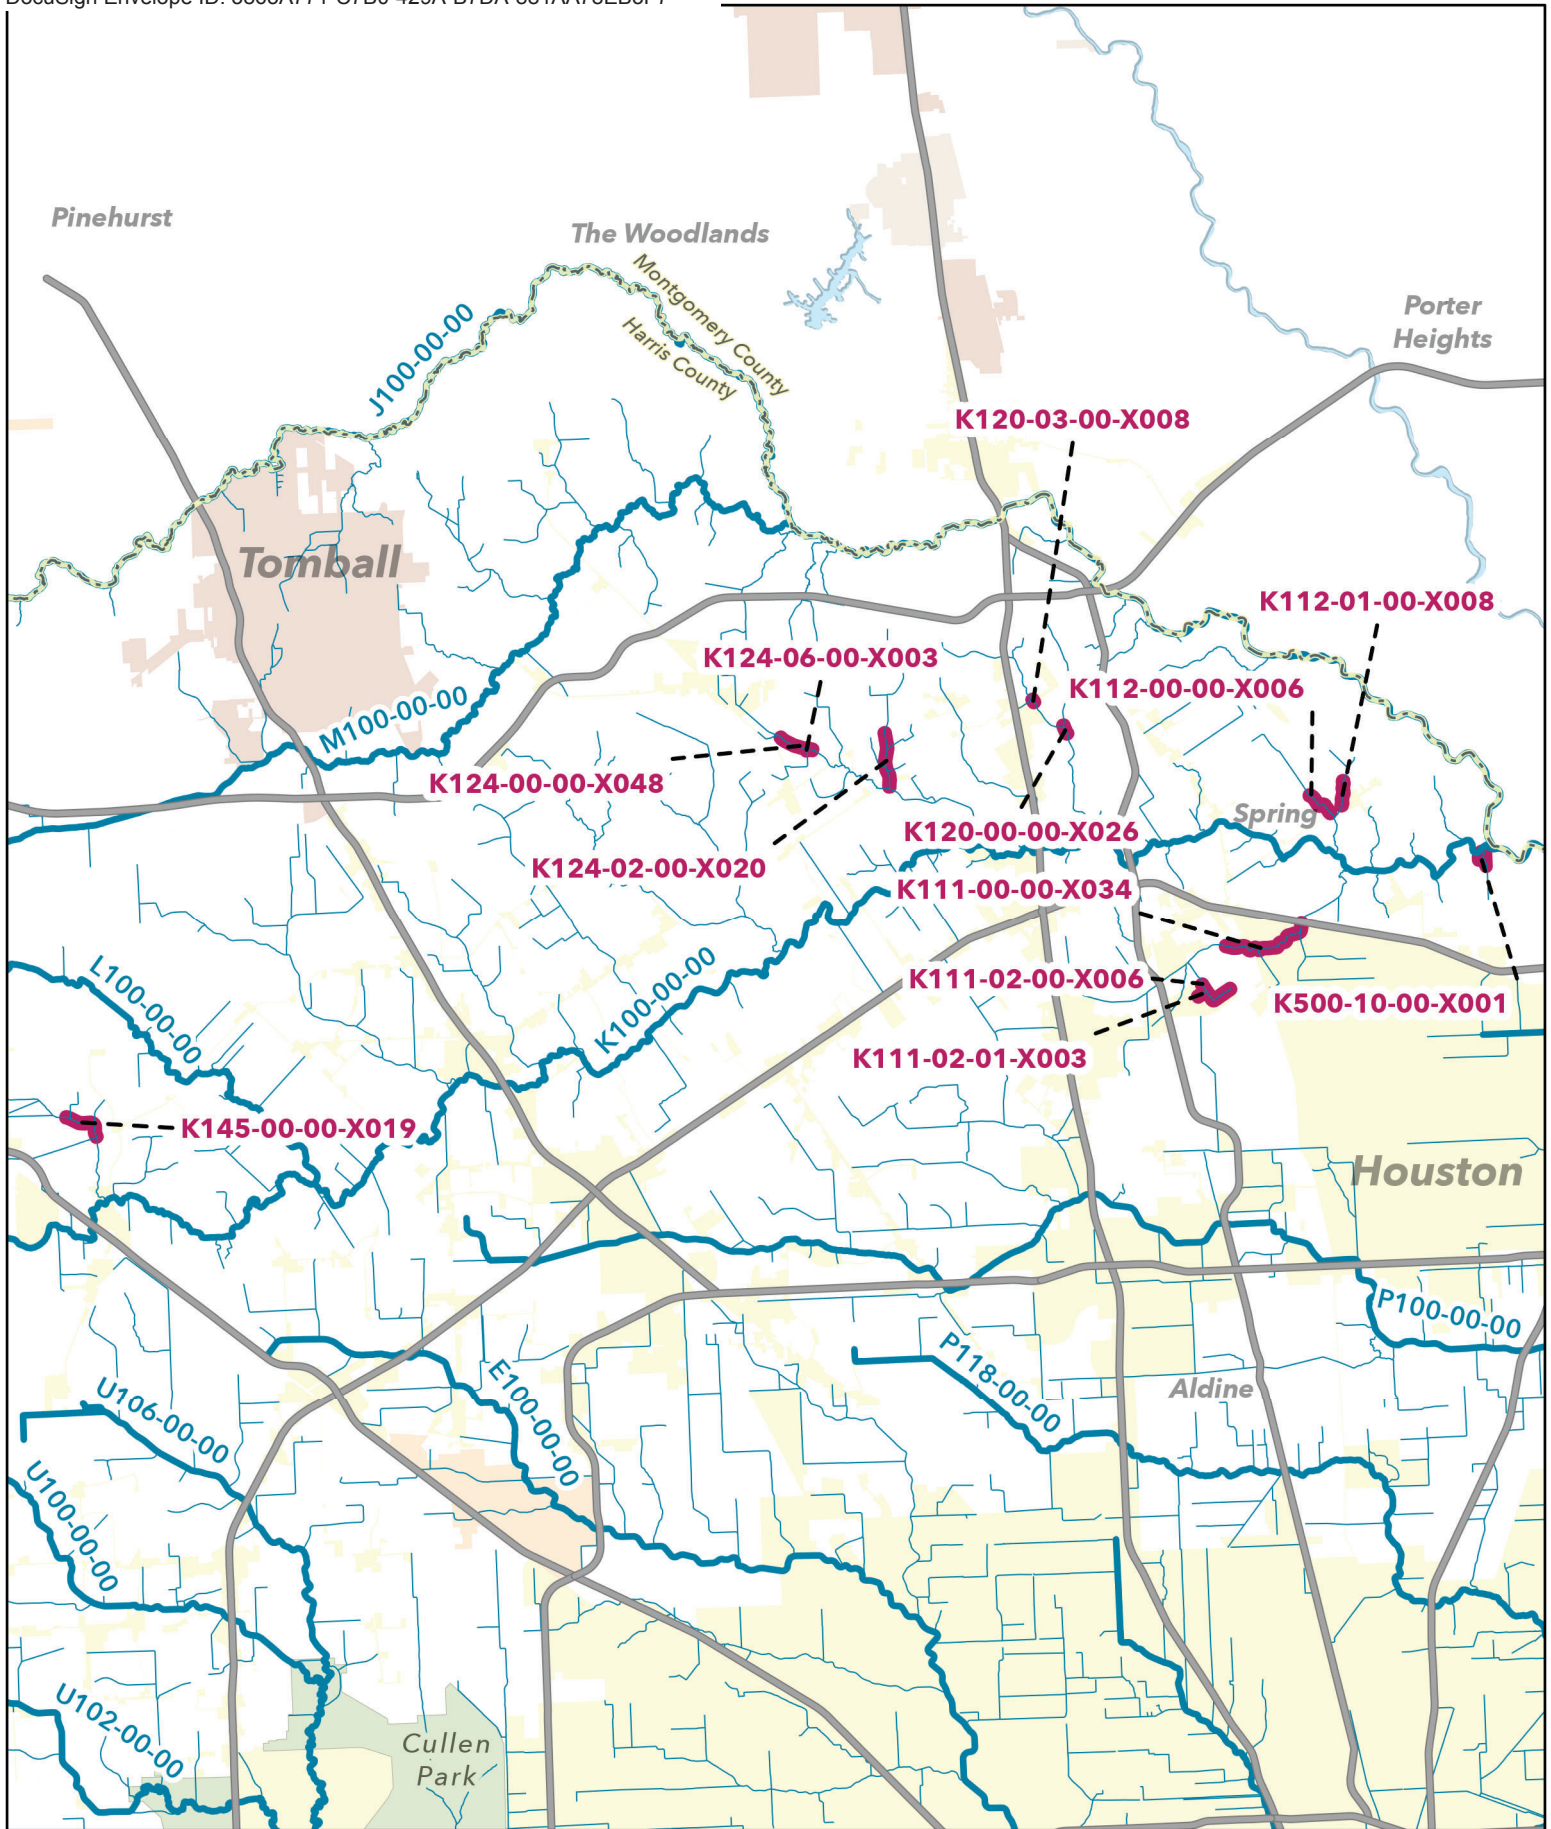

Project ID: K100-00-00-X087
Watershed: Cypress Creek
Precinct: 1, 3
